

FILE

26



Norfolk Southern Corporation
Communications and Signal Department
1200 Peachtree Street, N.E.
Atlanta, Georgia 30309-3579
404/529-1216

RECEIVED-DOCKETING DIV
2007 FEB 12 AM 9:44
PUCO

February 6, 2007
061-10.0492

06-1326-RR-FED

Ms. Susan Kirkland
Ohio DOT
1980 W. Broad St.
Columbus, OH 43223

RE: In the Matter of the Implementation of the Norfolk Southern Corridor Safety Project
"CJ" Line from Columbus, OH to Cincinnati, OH

Dear Ms. Kirkland:

Per the ORDC letter dated November 1, 2007, regarding the above case for the upgrade of automatic grade crossing warning devices at Snyder Street in Springfield, Clark County, Ohio, DOT: 523 506J, Milepost CJ-184.93.

Although we cannot give you an exact date of installation at this time we can provide our average installation time, which is 9.1 months after authorization from the state. After this project is authorized, we will order material and schedule for installation once we have received approvals from ODOT's district office.

An extra copy of this letter is included with the enclosures. Please date stamp this extra copy and forward to Mr. R. S. Noe, Assistant General Attorney, Norfolk Southern Corporation, Three Commercial Place, Norfolk, Virginia, 23510.

Upon receipt of this revised material, please initial, date and confirm via fax to 404-527-2901.

Sincerely,

B. L. Sykes

B. L. Sykes

Enclosure(s)

BLS/rhr/cp/rjs

Cc: Mr. R. S. Noe, NS Corporation, Norfolk, VA
✓ Ms. Bonnie Johrendt, PUCO (w/plans, estimate and material list)
Mr. Tim Perkins (w/plans, estimate and material list)
Docketing Division (w/plans, estimate and material list)
Ms. P. A. Gray, NS Corporation, Roanoke, VA (w/estimate)

RECEIVED
PUBLIC UTILITIES
COMMISSION OF OHIO
2007 FEB -9 PM 12:33
RAIL DIVISION

This is to certify that the images appearing are an accurate and complete reproduction of a case file document delivered in the regular course of business.
Technician *AW* Date Processed *2/12/07*



05-Feb-07

Detailed Estimate for Grade Crossing Warning Devices

City/State: SPRINGFIELD, OH

Road: SNYDER ST.

MilePost: CJ-184.93

DOT/AAR: 523506J

State Proj. No.:

County: CLARK

S&E Proj. No.: 10.1004

AFE: F10119

Man Days: 112

File Number: 061-10.0492

Purchases - Others	
Meals and Lodging:	\$10,538.04
Rental of Equipment:	\$23,038.40
(2 Trucks, 1 Backhoe w/ Trailer and 1 Pipe-Pusher for 28 Days)	
Construction Supervision Vehicle:	\$1,843.07
Purchases - Other Total:	\$35,419.51
Material And Additives	
Material Cost:	\$71,595.00
Sales and Use Tax:	\$0.00
Material Handling Freight:	\$3,579.75
Material Total:	\$75,174.75
Labor And Additives	
Labor Cost:	\$27,104.00
(4 man crew at \$968.00 a day for: 28 days)	
Payroll Tax & Overheads:	\$26,738.10
Preliminary Engineering:	\$8,685.51
Construction Supervision:	\$7,651.46
Labor Total:	\$70,179.07
Project Cost:	\$180,773.33
Scrap / Salvage Credit:	\$0.00
Project Total:	\$180,773.33

Estimated on: 05-Feb-07

Estimated by: ndr3j

Estimate valid for 1 year from date of estimate



Norfolk Southern Railway
Highway Crossing Signalization Program - Material List

Do not substitute items without permission from S & E Engineering

City:	SPRINGFIELD
Road:	SNYDER ST.
Mile Post:	CJ-184.93
Drawing Number:	82111850
State Project Number:	
County:	CLARK
A A R Number:	523506J
Project Number:	10.1004
File Number:	061-10.0492
New File Number:	
A F E Number:	F10119
Store Number:	07863
Supervisor:	D.M. FRANCIS
Tax Code:	3500
Vendor to supply the following copies after pricing: 1 Set - Material Management with original Invoice 2 Sets - with plans shipped in car with material 1 Set - S&E Gen. Supt. Construction w/copy of invoice	

Location: SPRINGFIELD			OH	S&E Proj. No.: 10.1004	AFE No.: F10119	Drawing No.: 82111850			
Store No.: 07863			P.O. Number:		Date Required:	Date Shipped:	Vendor: SW Signal Engineering Company		
Qty.	Class-Item-CD	UI	Price per Item	Total Price	Item Description	Quantity Shipped	Quantity Installed Date Quan.	Quantity Returned (Credit)	Special Instructions
3	670-350693-4	EA	\$5.04	\$15.12	AAR/DOT NUMBER PLATE/DECAL, ORDER 3 PER PROJECT. 60 DAY LEAD TIME. SUPPLIED BY STRAN.				
1	165-006505-4	EA	\$1,051.54	\$1,051.54	AC SERVICE, COMPLETE LESS METER BASE, ASSEMBLED ON 30' POLE				
8	670-119241-4	EA	\$32.80	\$262.40	ARRESTOR, LIGHTNING HEAVY DUTY CLEAR VIEW SAFETRAN 022585-1X				
13	105-871901-4	EA	\$161.57	\$2,100.41	BATTERY,GNB 265AH MODEL 50A11 SINGLE CELL 2.25 VOLTS				
2	670-980689-4	EA	\$71.71	\$143.42	BRACKET HIGH WIND, (RIGID 3'), WIG- 191036, WALRUS TUSK TYPE				
2	670-561375-4	EA	\$1,197.90	\$2,395.80	BRACKET, GATE SAVER, NEG385102GS, SPRING LOADED SWING AWAY ADAPTER FOR FIBERGLASS/ALUMINUM GATES, USE WITH GATE 28' AND LESS				
1	670-356949-4	EA	\$97.00	\$97.00	CABLE, 10' GENERATOR HOOK UP, SERRMI P/N 40524, FEMALE CONNECTOR				
300	465-292862-4	LF	\$1.04	\$312.00	CABLE, U-2-6 TWISTED, S-23 OKONITE 113-12-3933 SOLID TINNED CONDUCTOR				
800	465-292945-4	LF	\$1.35	\$1,080.00	CABLE, U-5-14, S-54 OKONITE 206-14-6885				
300	465-292929-4	LF	\$3.05	\$915.00	CABLE, U.G. 5 COND. NO. 6 AWG SOLID COPPER CABLE TO MEET NS CORP. SPEC. FOR SIGNAL				
600	465-939422-4	LF	\$2.55	\$1,530.00	CABLE, UG 12 CONDUCTOR NO 14 AWG SOLID EACH CONDUCTOR WITH 5/64 IN INSULATION 10 MIL				
300	465-791835-4	FT	\$2.22	\$666.00	CABLE, UG AC ENTRANCE 3C#6-7X OKONITE FMF-L 094-078 TR W/G 1 X 8 7X W010 BRZ TAPE 600V PRODUCT CODE 206-11-6070				
120	165-544477-4	FT	\$2.55	\$306.00	CONDUIT, 4"x10' PVC, SCHEDULE 80 BELL CONNECTOR AT ONE END, 1/2 PT. GLUE IN KIT 670-123298-4				
2	670-090450-4	EA	\$50.38	\$100.76	CONNECTOR, WELDED FAR RAIL HARMON A1000-2W				
2	670-486846-4	EA	\$41.62	\$83.24	CONNECTOR, WELDED NEAR RAIL HARMON A1000-1W				
2	670-793404-4	EA	\$838.37	\$1,676.74	COUNTERWEIGHT PKAGE, 17-24'GATE STRAN S- MECH ONLY, STAINLESS, TO INCLUDE HUB, SUPPORT ARMS				
4	670-760012-4	EA	\$40.02	\$160.08	COVER, FOR 1 WAY FLASHING LIGHT ASSY. 18 OZ. BLACK VINYL COATED NYLON. ===== TO COVER 2 LAMPS=====				

APPROVED BY STATE	APPROVED BY RAILROAD	CAR NUMBER	SEAL NUMBER
-------------------	----------------------	------------	-------------

Qty.	Class-Item-CD	U/I	Price per item	Total Price	Item Description	Quantity Shipped	Quantity Installed Date Quan.	Quantity Returned (Credit)	Special Instructions
1	670-988650-4	EA	\$375.69	\$375.69	DISPOSAL, CONSTRUCTION DEBRIS AND CLEANING X'ING EQUIPMENT CONTAINER				
1	670-000004-4	EA	\$700.00	\$700.00	FCC LICENSE FOR MONITOR/RADIO				
5	670-000003-4	EA	\$255.85	\$1,279.25	FILL/STONE #57, QUANTITY IS BASED ON TRUCK LOAD PLUS DELIVERY COST				
2	670-015231-4	EA	\$423.50	\$847.00	FOUNDATION, DIXIE, S-2 GATE 56" ASSEMBLED				
2	670-257031-4	EA	\$297.88	\$595.76	GATE, ARM FIBERGLASS-ALUMINUM 17-24 FT., INCLUDES GATE GUARD FOR GATE LIGHT CABLE, NEG P/N 8002-244NFS/CG				
1	670-730154-4	EA	\$43.57	\$43.57	INDUCTOR, SIMULATED TRACK SAFETRAN 8V617-2000				
1	670-477991-4	EA	\$317.90	\$317.90	KIT, GROUNDING ASSY FOR AL I/S INCLUDES 8 GRD RDS, 200#4 WIRE, 12 4 WIRE ONE-SHOTS. ERICO 59K206				
1	670-123298-4	EA	\$256.93	\$256.93	KIT, HARDWARE SUPPLIES REQUIRED X'ING P'CKAGES. WEB CONNECTORS FOR SHUNT(8EA) TAPE, AMPS, P'GUM PAINT, SLEEVES, TAGS, GLUE, 100 EA WHITE TAGS,)NE CAN BLUE MARKING PAINT ETC...				
2	670-764166-4	EA	\$907.65	\$1,815.30	LAMP ASSY, 5" MAST MTG. 2W IND. 20" BKGRD, FLX-12 W/BULB STRAN #042003-487XNS				
6	165-643547-4	EA	\$4.30	\$25.80	LAMP, 18 WATT 10 VOLT S-11 SC BAY 18S11/1SC CLEAR RWY SIGNAL UJ-71463 GE				
8	670-440826-4	EA	\$1.01	\$8.08	LINK, SAFETRAN 024620-1X INSL TESTING COMP 1 IN CENTER SIGNAL CIRCUITS CR 02-286662				
4	255-590880-4	EA	\$16.12	\$64.48	LOCK, AMERICAN LOCK MODEL H-10KA KEYS ALIKE TO PRIVATE KEYWAY D456 AND STAMPED "NS SIG"				
2	670-637778-4	EA	\$1,031.41	\$2,062.82	MAST, 5" ALUMINUM 13'10" WITH DOUBLE JCT. BOX BASE. STRAN P# 070519-11AX.				
2	670-850933-4	EA	\$3,352.65	\$6,705.30	MECHANISM, GATE MODEL S-60, WITH DEFROSTER AND MINI TRACKSIDE SENSOR S'TRAN # 0740007-X002B3				
7	670-000001-4	EA	\$316.23	\$2,213.61	MISC. MATERIAL				
2	670-001347-4	EA	\$63.27	\$126.54	PACKAGE, HARDWARE SIGN 5 IN. MOUNTING, SERRMI A1250-5, HARMON @200965-000, OR				

APPROVED BY STATE APPROVED BY RAILROAD CAR NUMBER SEAL NUMBER


Qty.	Class-Item-CD	UI	Price per Item	Total Price	Item Description	Quantity Shipped	Quantity Installed Date Quan.	Quantity Returned (Credit)	Special Instructions
1	255-646807-4	EA	\$10.38	\$10.38	PADLOCK, SAFETRAN PART NO. 030399-29X SCREW TYPE FOR CIR CONTROLLER AND BTY. BOX				
1	610-719870-4	EA	\$135.90	\$135.90	PEDESTAL ASSEMBLY, ARMORCAST P/N P6001205-NS, YELLOW 10"X11"X28" POLYETHYLENE INCL 45" WITH TERMINAL BLOCK				
1	670-514605-4	EA	\$8.45	\$8.45	PINNACLE, W-C SECT 1-11, 4" & 5" REF K1 110-8 OR SAFETRAN NO. @035045-503X				
2	670-555609-4	EA	\$45.12	\$90.24	PLUGBOARD, TYPE B-1 GRS A62-506 OR HARMON @7062-506 OR				
1	670-427136-4	EA	\$93.49	\$93.49	POWER OFF LAMP INDICATOR FOR SHELTER, SAFETRAN P/N 051958-5				
1	165-902002-4	EA	\$308.00	\$308.00	PROTECTOR, SURGE 120/240VAC, ERICO P/N EPD120/240TDFL				
5	465-002899-4	EA	\$22.06	\$110.30	REEL, CABLE DISPOSABLE FOR CROSSING SIGNAL PACKAGES				
1	670-742096-4	EA	\$41.80	\$41.80	RELAY INTERFACE PROBE, ULTRATECH PN 16031-00				
2	670-707995-4	EA	\$313.67	\$627.34	RELAY, TYPE B1, NEV LINE, 900 OHMS, .008 AMPERES GRS A62-308 OR SAFETRAN @400003				
2	435-805560-4	EA	\$6.25	\$12.50	SAND, 25LB BAG FOR CABLE ENTRANCE INTO THE SHELTER				
1	670-816502-4	EA	\$4,903.75	\$4,903.75	SEARII AUTOMATED INSPECTOR SYSTEM KIT, w/ 1-ILOD, 1-eBELL, 2-GTS, WITHOUT MTSS, 1-GFT, 1-VHFC, 2- RECORDER INTERFACE MODULE, 1-ECHELON CONNECTOR				
1	670-281280-4	EA	\$7,006.00	\$7,006.00	SHELTER BARE 6X6, ALUMN, FARADAY, W/CABLE CHUTES BEHIND TERMINAL BOARD, W/GEN. CONN. W/ADJUSTABLE PIERS, SAFETRAN P/N 058400-66-78A				
2	670-586967-4	EA	\$37.68	\$75.36	SHUNT COVER W/LAG SCREWS, 19"X19", SERRMI #40271, ORDER 1 PER SHUNT				
2	670-775391-4	EA	\$438.32	\$876.64	SHUNT, MULTI-FREQ. #62780-1543 SAFETRAN NARROW BAND-LOW LOADING				
2	670-393331-4	EA	\$37.43	\$74.86	SIGN CROSSING MALFUNCTION ASSEMBLY FOR 4" AND 5" MAST, SAFETRAN #117215				
2	670-806648-4	EA	\$56.42	\$112.84	SIGN, X-BUCK, LESS HARDWARE, SAFETRAN 035200-X CR 02-490546				

APPROVED BY STATE APPROVED BY RAILROAD CAR NUMBER SEAL NUMBER

Location: SPRINGFIELD			OH	S&E Proj. No.: 10.1004	AFE No.: F10119	Drawing No.: 82111850			
Store No.: 07863			P.O. Number:		Date Required:	Date Shipped:	Vendor: SW Signal Engineering Company		
Qty.	Class-Item-CD	UI	Price per Item	Total Price	Item Description	Quantity Shipped	Quantity Installed Date Quan.	Quantity Returned (Credit)	Special Instructions
1	670-330382-4	RL	\$15.68	\$15.68	TAPE, THOR 3" DURATEC, ORANGE 1000' LENGTHS. "WARNING STOP DIGGING"				
17	670-478560-4	EA	\$19.47	\$330.99	TERMINAL BLOCK, ERICO 4 POST P/N B2700A2C1WH W/HARDWARE LESS LIGHTNING ARRESTOR				
2	165-917984-4	EA	\$4.84	\$9.68	TERMINAL, TEST, TYPE B GRS A62-515 OR HARMON @ 32118-001 OR				
2	610-065626-4	EA	\$17.55	\$35.10	ULTRA-TECH 15206-01 CONNECTIVITY BLOCK FOR GRS B1 RELAY				
6	670-007238-4	EA	\$129.46	\$776.76	UNIT, THE INSTALLATION AND WIRING OF A DEVICE WHICH REQUIRE A MINIMUM OF FOUR WIRE CONNECT.				
1	670-258957-4	EA	\$25,580.50	\$25,580.50	WIRED RACK, 6X6 FARADAY, 20AMP SINGLE TRK SSCCHIA, GCP3000D2, 2 CRAGG CHARGER, 2 RELAY RACKS, SAFTRAN P/N 20A 1TRK, USE WITH I/S 670-281280-4 W/CABLE CHUTES BEHIND THE FARADAY SHIELD				
1	450-986008-4	EA	\$24.84	\$24.84	WRENCH, TEST POST TYPE B DWG 55393-3, GR.1				


Total Material: \$71,594.94

APPROVED BY STATE	APPROVED BY RAILROAD	CAR NUMBER	SEAL NUMBER
-------------------	----------------------	------------	-------------

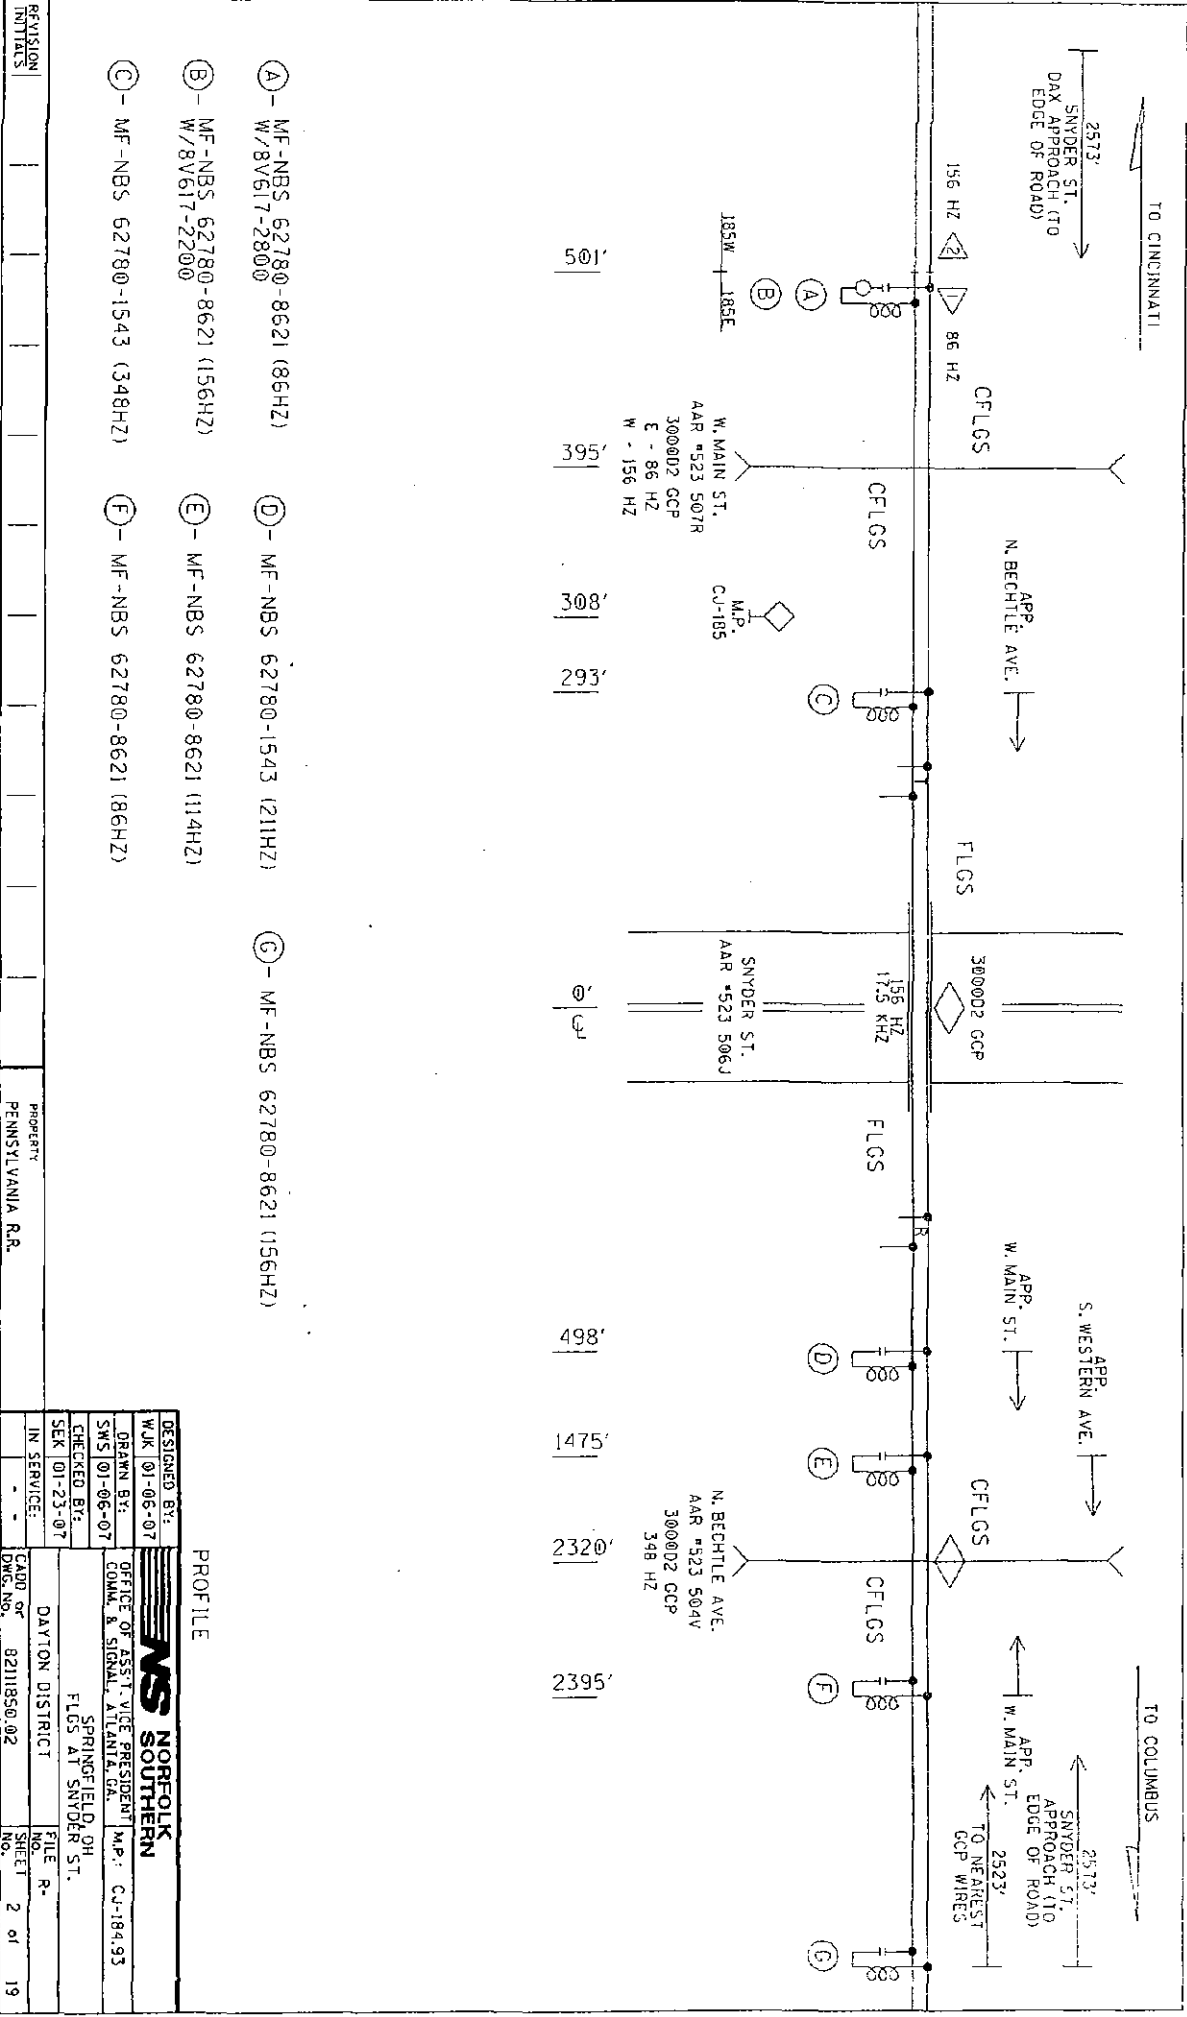


PROFILE

DESIGNED BY:	WJK 01-06-07	OFFICE OF ASST. VICE PRESIDENT	DATE: 01-18-93
DRAWN BY:	SWS 01-06-07	COMM. & SIGNAL, ATLANTA, GA.	
CHECKED BY:	SEK 01-23-07	SPRINGFIELD, OH	
IN SERVICE:		FLGS AT SNYDER ST.	
DAYTON DISTRICT		FILE R-	
CARD OF	8211850.02	SHEET	2 of 19

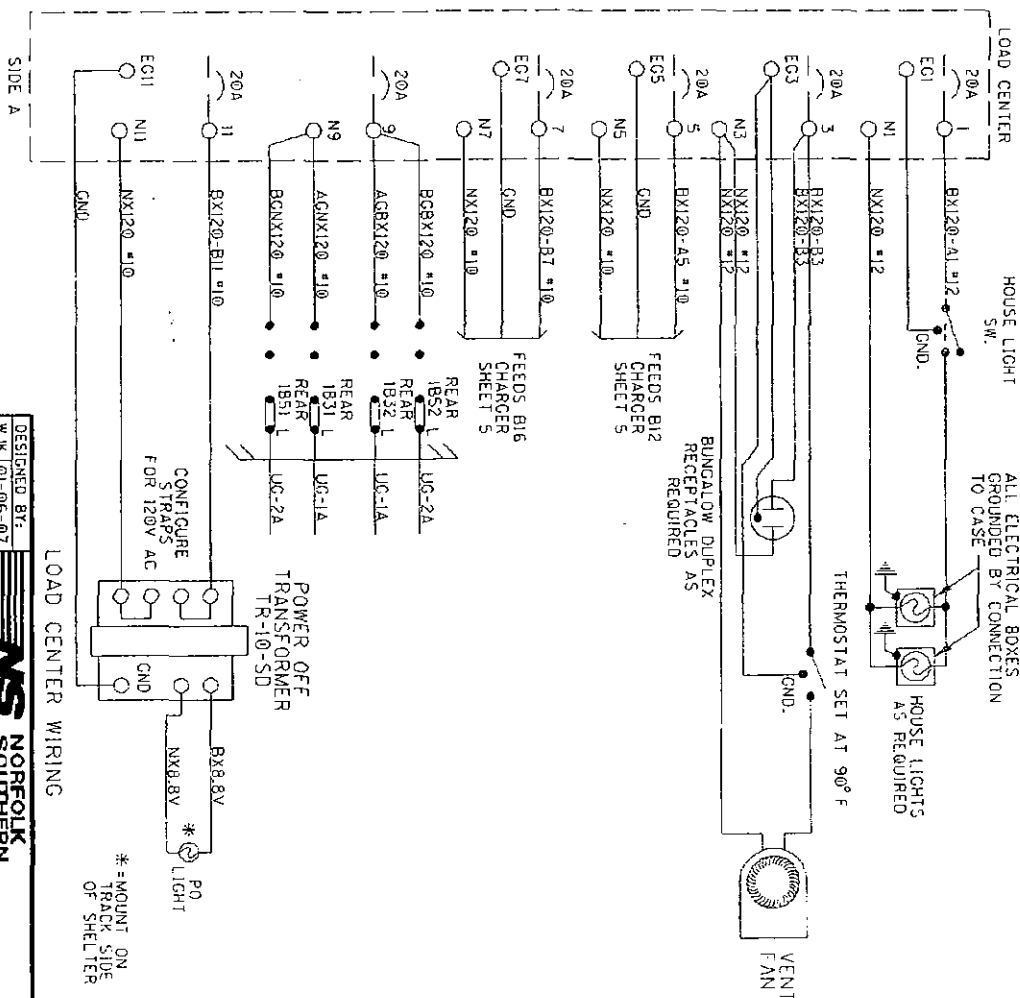

100A 2P CIR BKR --- Q02100
MECH INTERLOCK --- PK4DTMALA

DESIGNED BY:	WJM 01-06-07	OFFICE OF ASST. MGR PRESENTIAL COMM. & SIGNALS ANTENNA CO.	M.P.: C3-1B4.93
DRAWN BY:	SWS 01-06-07	SPRINGFIELD OH	
CHECKED BY:	SEK 01-23-07	FLOT AT SANDER ST.	
IN SERVICE:		DAYTON DISTRICT	
CADD OF PVC. NO.	8211850.04	FILE R-	
SHEET	4 of 19		

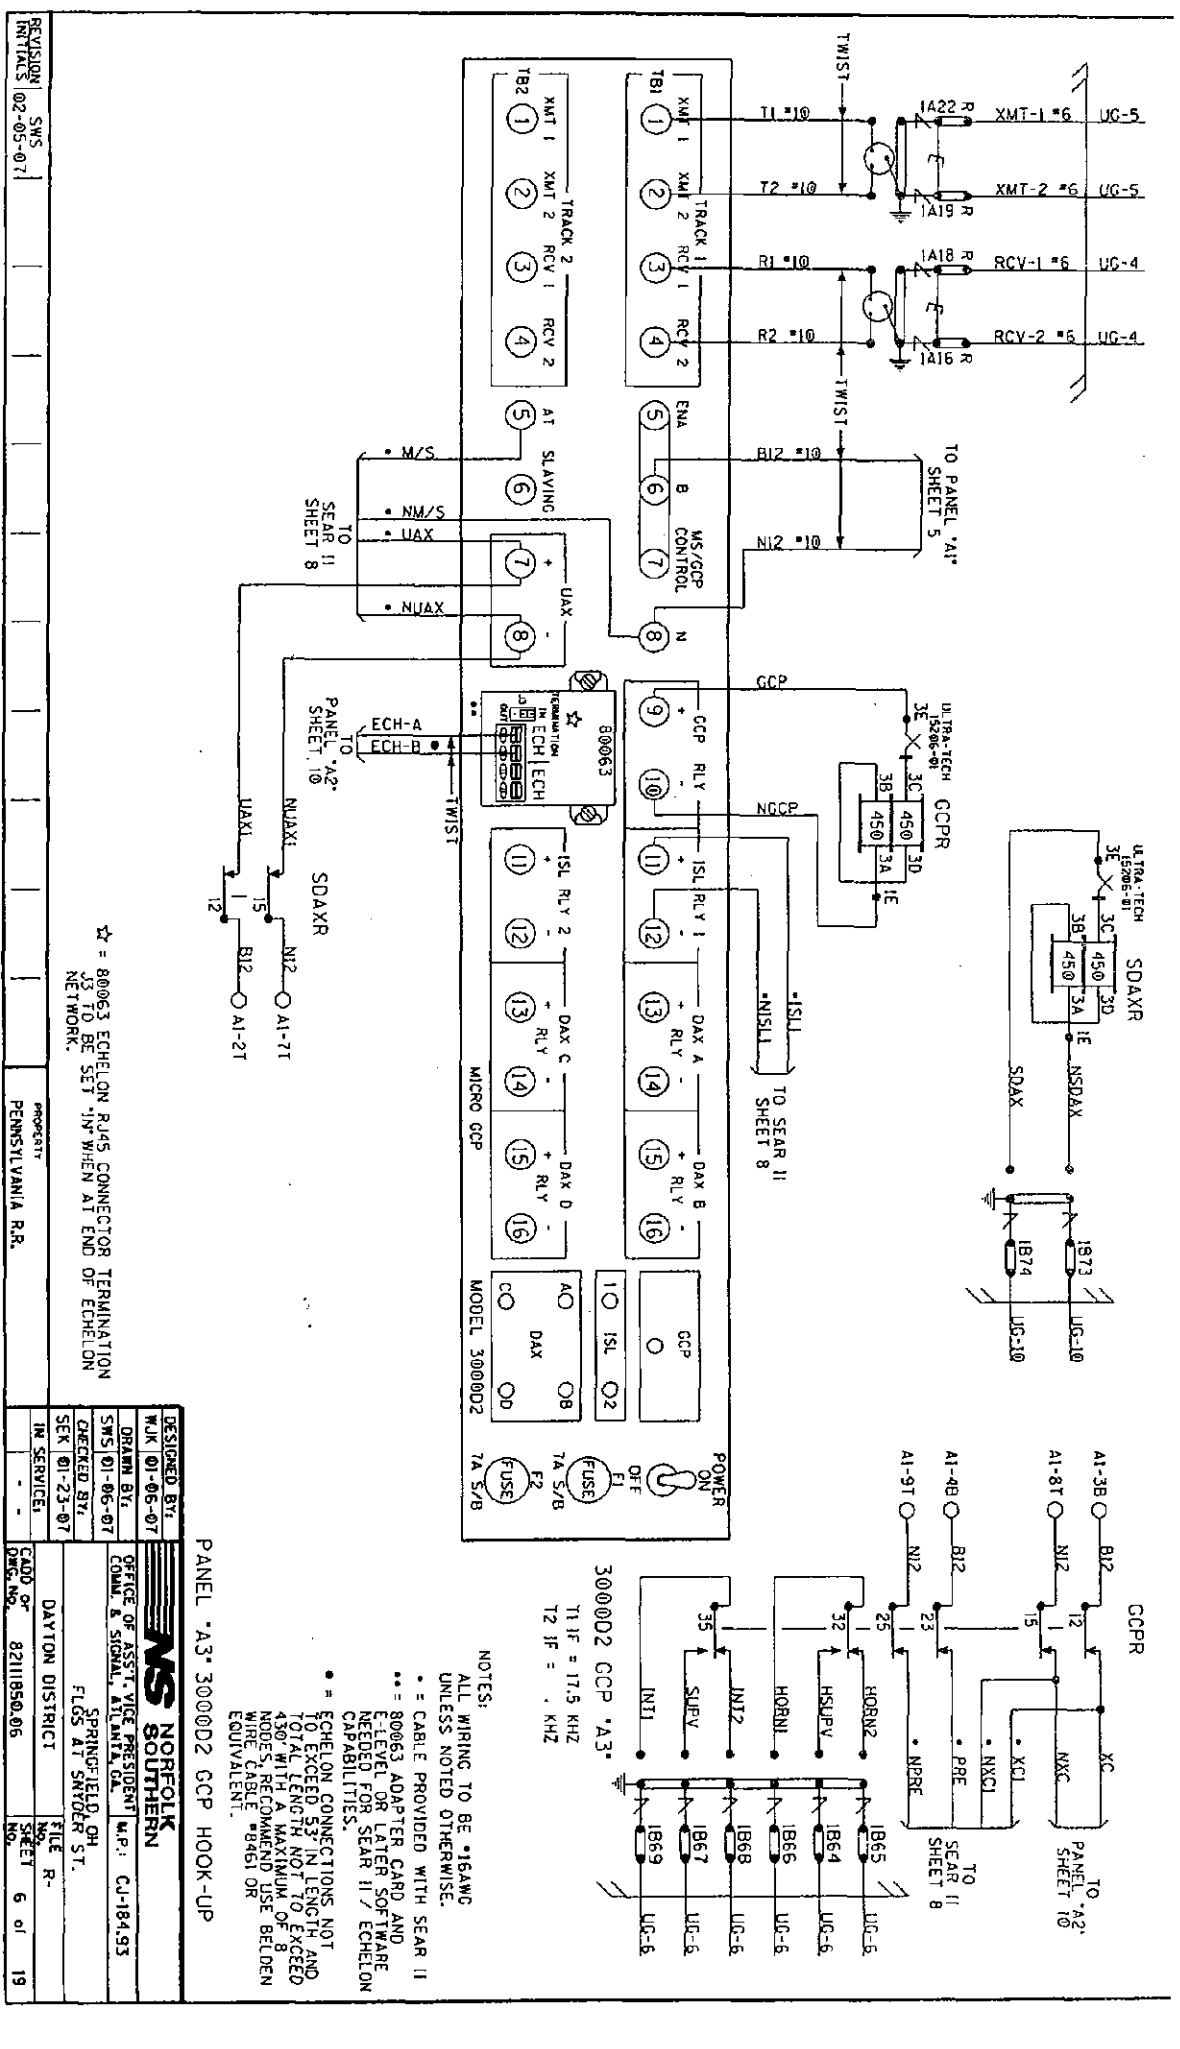

300002 PROGRAMMING CHART (LEVEL: 0)	
NUMBER OF TRACK TRANSCIVERS	1
T1: FREQUENCY	156HZ
T2: FREQUENCY	--HZ
T1: UNIDIRECTIONAL/BIDIRECTIONAL	81
T2: UNIDIRECTIONAL/BIDIRECTIONAL	---
T1: XMIT LEVEL (MAX/MED)	MAX
T2: XMIT LEVEL (MAX/MED)	---
T1: PREDICTOR/MOTION SENSOR	PRED
T2: PREDICTOR/MOTION SENSOR	---
T1: WARNING TIME	30 Sec
T2: WARNING TIME	---
T1: APPROACH DISTANCE	3523 Ft
T2: APPROACH DISTANCE	---
T1: PICKUP DELAY (UAX) (0 = OFF)	25 Sec
T2: PICKUP DELAY (UAX) (0 = OFF)	---
EMA/UAX DELAY (0 = EMA)	-- Sec
T1: ISLAND DISTANCE	148 Ft
T2: ISLAND DISTANCE	---
NUMBER OF DAX'S	0 Eq
DAX A TRACK ASSIGNMENT (T1/T2)	---
DAX A DISTANCE (0 = PREEMPT)	Ft
DAX B TRACK ASSIGNMENT (T1/T2)	---
DAX B DISTANCE (0 = PREEMPT)	Ft
DAX C TRACK ASSIGNMENT (T1/T2)	---
DAX C DISTANCE (0 = PREEMPT)	Ft
DAX D TRACK ASSIGNMENT (T1/T2)	---
DAX D DISTANCE (0 = PREEMPT)	Ft
DAX D WARNING TIME	Sec
GLAVING (MASTER/SLAVE)	MASTER
PASSWORD ENABLED	NO
RECORDER INSTALLED	NO

EXPANDED PROGRAMMING

T1: SWITCH TO MS (ENTER E2 VALUE)	10 %
T2: SWITCH TO MS (ENTER E2 VALUE)	-- %
T1: TRANSFER DELAY MS TO GCP (0 = OFF)	0 Sec
T2: TRANSFER DELAY MS TO GCP (0 = OFF)	-- Sec
T1: TRANSFER MS TO GCP PRIME (ON/OFF)	---
T2: TRANSFER MS TO GCP PRIME (ON/OFF)	---
T1: TRANSFER MS TO GCP DAX A (ON/OFF)	---
T2: TRANSFER MS TO GCP DAX A (ON/OFF)	---
T1: TRANSFER MS TO GCP DAX B (ON/OFF)	---
T2: TRANSFER MS TO GCP DAX B (ON/OFF)	---
T1: TRANSFER MS TO GCP DAX C (ON/OFF)	---
T2: TRANSFER MS TO GCP DAX C (ON/OFF)	---
T1: TRANSFER MS TO GCP DAX D (ON/OFF)	---
T2: TRANSFER MS TO GCP DAX D (ON/OFF)	---
T1: PRIME PREDICTION OFFSET (0 = OFF)	-- Ft
T2: PRIME PREDICTION OFFSET (0 = OFF)	---
T1: PICKUP DELAY PRIME	15 Sec
T2: PICKUP DELAY PRIME	---
PICKUP DELAY DAX A	-- Sec
PICKUP DELAY DAX B	-- Sec
PICKUP DELAY DAX C	-- Sec
PICKUP DELAY DAX D	-- Sec
T1: ENHANCED DETECTION (ON/OFF)	OFF
T2: ENHANCED DETECTION (ON/OFF)	---
BACK-TO-BACK T1 AND T2 (NO/YES)	---
T1: STATION STOP TIMER	-- Sec
T2: STATION STOP TIMER	-- Sec
T1: NUMBER OF TRACK WIRES (4/6)	4
T2: NUMBER OF TRACK WIRES (4/6)	---
T1: LOW EX ADJUSTMENT	0
T2: LOW EX ADJUSTMENT	---
T1: LOW E2 DETECTION	OFF
T2: LOW E2 DETECTION	---
T1: LOW E2 DETECTION TIMER (ON/OFF)	-- Min
T2: LOW E2 DETECTION TIMER (ON/OFF)	-- Min
T1: POSITIVE START (E2 LEVEL) (0 = OFF)	0
T2: POSITIVE START (E2 LEVEL) (0 = OFF)	---
T1: POSITIVE START TIMEOUT (0 = NONE)	-- Min
T2: POSITIVE START TIMEOUT (0 = NONE)	-- Min
SET AT OPERATION (NORMAL/DIAGNOSTIC)	NORMAL
DAX MESSAGES (ON/OFF)	ON
ADVANCE PREEMPT TIMER (0 = OFF)	0
T1: MOTION SENSING LEVEL (0 = NORMAL)	0 %
T2: MOTION SENSING LEVEL (0 = NORMAL)	-- %

(1)
(2)
(2)
(2)
(2)
(2)
(2)
(2)
(2)
(2)
(2)
(2)

* = 1ST SLOT AT LEFT END OF BAY

MODEL 300002 GCP MODULE ASSEMBLIES											
UPPER BAY											
MODULES POSITION	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11
MODULE NUMBERS	80211-f(1) * ISL	80211-f(2) ISL	80012 T/R 1	80012 T/R 2	80013 RLY DRV	80214 PROCS	80255 REC-INTF	80016 (1) DAX	80016 (2) DAX	80020 +80017	80211-f(1) * ISL
MODULES USED	X	X	X	X	X	X	X	X	X	X	X
LOWER BAY											
MODULES POSITION	M12	M13	M14	M15	M16	M17	M18	M19	M20	M21	M22
MODULE NUMBERS	80012 T/R 1	80012 T/R 2	80013 RLY DRV	80214 PROCS	80255 REC-INTF	80016 (1) DAX	80016 (2) DAX	80020 +80017	80028 XFRTL/R		
MODULES USED	X	X	X	X	X	X	X	X	X	X	X

NOTES:
1 - SEE IPI INSTRUCTION AND INSTALLATION MANUAL FOR 80211 ISLAND CALIBRATION PROCEDURE.
2 - TOGGLE SWITCH ON MOTHER BOARD:
UP = DUAL FREQ.
DOWN = SINGLE FREQ.


** = 80214 & 80255 (WITH JUMPER) CARDS AND E-LEVEL OR LATER SOFTWARE NEEDED FOR SEAR II / ECHOLON CAPABILITIES.

PANEL 'A3' 300002 GCP SET-UP

- 300002 PROGRAMMING NOTES:
- 1) AVAILABLE WHEN *TRANSFER DELAY MS TO GCP* AND *PRIME PREDICTION OFFSET* IS ON
 - 2) AVAILABLE WHEN *TRANSFER DELAY MS TO GCP* AND DAX DISTANCE IS GREATER THAN ZERO
 - 3) AVAILABLE WHEN *ENHANCED DETECTION* IS ON
 - 4) AVAILABLE WHEN *LOW E2 DETECTION* IS ON
 - 5) AVAILABLE WHEN *POSITIVE START* IS ON

PROPERTY
PENNSYLVANIA R.R.

DESIGNED BY:	WJK 01-06-07	OFFICE OF ASST. VICE PRESIDENT	W.P.: C-184.93
DRAWN BY:	SWS 01-06-07	COMM. & SIGNAL, ATLANTA, GA.	
CHECKED BY:	SEK 01-23-07	SPRINGFIELD OH	
IN SERVICE:		FLGS AT SNYDER ST.	
CADD or DWG. No.	8211850.07	DAYTON DISTRICT	FILE R-
			SHEET 7 of 19

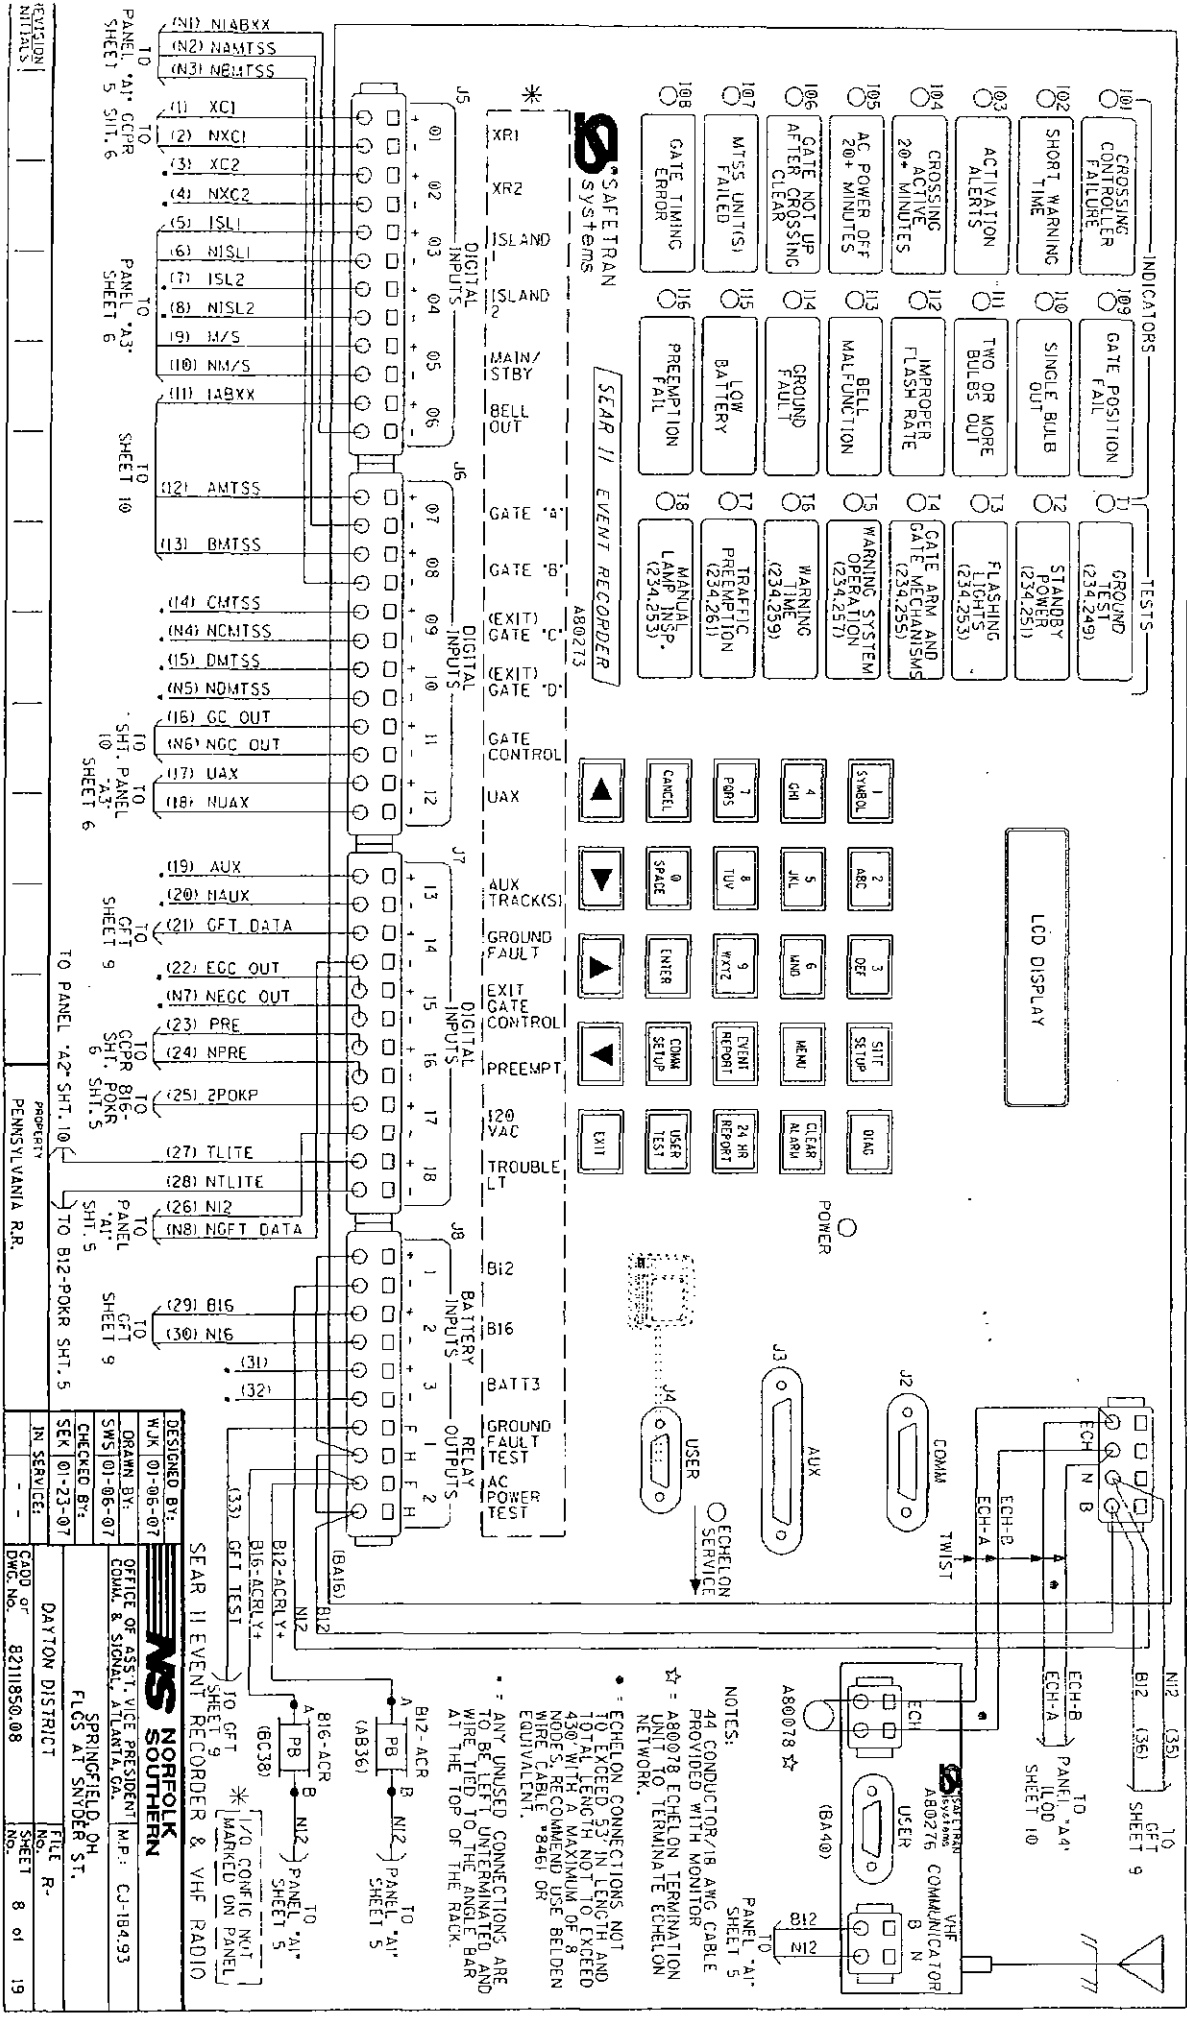

DESIGNED BY: WOK 01-06-07
DRAWN BY: SWS 01-06-07
CHECKED BY: SEC 01-23-07
DAYTON DISTRICT
FILE NO. 8 of 19
DWC No. 8211850.08


NOTES:
44 CONDUCTOR/18 AWG CABLE PROVIDED WITH MONITOR UNITS TO TERMINATE ECHOLON NETWORK.
★ = A80078 ECHOLON TERMINATION EQUIVALENT.
• ECHOLON CONNECTIONS NOT TO EXCEED 53' IN LENGTH AND TOTAL LENGTH NOT TO EXCEED 430' WITH A MAXIMUM OF 8 NODES. RECOMMEND USE BELDEN WIRE CABLE #8461 OR EQUIVALENT.
• ANY UNUSED CONNECTIONS ARE TO BE LEFT UNTERMINATED AND AT THE TOP OF THE RACK.

SEAR II EVENT RECORDER & VHF RADIO
SHEET 9
TO GFT SHEET 9
TO GFT SHEET 10
TO GFT SHEET 11
TO GFT SHEET 12
TO GFT SHEET 13
TO GFT SHEET 14
TO GFT SHEET 15
TO GFT SHEET 16
TO GFT SHEET 17
TO GFT SHEET 18
TO GFT SHEET 19
TO GFT SHEET 20
TO GFT SHEET 21
TO GFT SHEET 22
TO GFT SHEET 23
TO GFT SHEET 24
TO GFT SHEET 25
TO GFT SHEET 26
TO GFT SHEET 27
TO GFT SHEET 28
TO GFT SHEET 29
TO GFT SHEET 30
TO GFT SHEET 31
TO GFT SHEET 32
TO GFT SHEET 33
TO GFT SHEET 34
TO GFT SHEET 35
TO GFT SHEET 36
TO GFT SHEET 37
TO GFT SHEET 38
TO GFT SHEET 39
TO GFT SHEET 40
TO GFT SHEET 41
TO GFT SHEET 42
TO GFT SHEET 43
TO GFT SHEET 44
TO GFT SHEET 45
TO GFT SHEET 46
TO GFT SHEET 47
TO GFT SHEET 48
TO GFT SHEET 49
TO GFT SHEET 50
TO GFT SHEET 51
TO GFT SHEET 52
TO GFT SHEET 53
TO GFT SHEET 54
TO GFT SHEET 55
TO GFT SHEET 56
TO GFT SHEET 57
TO GFT SHEET 58
TO GFT SHEET 59
TO GFT SHEET 60
TO GFT SHEET 61
TO GFT SHEET 62
TO GFT SHEET 63
TO GFT SHEET 64
TO GFT SHEET 65
TO GFT SHEET 66
TO GFT SHEET 67
TO GFT SHEET 68
TO GFT SHEET 69
TO GFT SHEET 70
TO GFT SHEET 71
TO GFT SHEET 72
TO GFT SHEET 73
TO GFT SHEET 74
TO GFT SHEET 75
TO GFT SHEET 76
TO GFT SHEET 77
TO GFT SHEET 78
TO GFT SHEET 79
TO GFT SHEET 80
TO GFT SHEET 81
TO GFT SHEET 82
TO GFT SHEET 83
TO GFT SHEET 84
TO GFT SHEET 85
TO GFT SHEET 86
TO GFT SHEET 87
TO GFT SHEET 88
TO GFT SHEET 89
TO GFT SHEET 90
TO GFT SHEET 91
TO GFT SHEET 92
TO GFT SHEET 93
TO GFT SHEET 94
TO GFT SHEET 95
TO GFT SHEET 96
TO GFT SHEET 97
TO GFT SHEET 98
TO GFT SHEET 99
TO GFT SHEET 100

SITE SET UP PROCEDURE	
FUNCTION	LED DISPLAY
DATE	- - - -
TIME	- - - -
DAYLIGHT SAVINGS TIME	YES
TIME ZONE	EST
SITE NAME	SNYDER ST.
DOT NUMBER	523 506J
MILEPOST	CJ-184.93
TESTER TYPE	CROSSING
DATE FORMAT	MM-DD-YYYY
TEMP FORMAT	FAHRENHEIT
SITE TYPE	NO COMMUNICATION
SITE ATCS	7ARRALL.GCG.03.01
OFFICE ATCS ADDRESS	25500.01.9100
POLL ID	1
OFFICE FB/F9	YES
OFFICE COMM DEVICE	SPREAD SPECTRUM RADIO
DIAL MODEM PORT	AUX/COMM
PHONE NUMBER	(OFFICE NUMBER)
INIT STRING	(LEAVE BLANK)
BACKUP SITE ADDRESS 1	
BACKUP SITE ADDRESS 2	
FIELD COMM	
USER PORT	BAUD 57600, N. B. 1, NONE
AUX PORT	BAUD 9600, N. B. 1, NONE
COMM PORT	BAUD 9600, N. B. 1, NONE

VERIFY NUMBER OF BULBS	8 BULBS
CURR 1: LAMP SET UP	8 BULBS
CURR 2: LAMP SET UP	8 BULBS

CONTROL SYSTEM CONFIGURATION MENU QUESTIONS	
THE QUESTION	SELECT FROM MENU OPTION
RESET NAMES AND MODULES?	YES
NUMBER OF TRACKS?	1
NUMBER OF XR INPUTS?	1
CONSTANT WARNING DEVICE	GCP
CROSSING CONTROLLER?	SSCC III (A, PLUS)
MAIN / STANDBY	YES
AUXILIARY TRACKS?	NO
AUX TRACK	(SET IF AUX TRACKS = YES)
GATES?	2
EXIT GATES?	0
UAX?	DROPS MD/GCP
BATTERY BANKS?	2
PREEMPTION?	YES
110D MODULES?	1
LAMP TYPE?	NORMAL
AUTO INSPECTIONS?	YES
BELL SENSOR?	** 1
BELL SENSOR INPUT 7	** YES
BELL SENSOR INPUT 8	** NO
BELL SENSOR INPUT 9	** NO
BELL SENSOR INPUT 10	** NO
BELL ON?	GATES LOWERING
GATE TIP SENSORS?	YES
GROUND FAULT DETECTORS?	YES
CHANNEL 1	161.475 MHZ
CHANNEL 2	NONE
FULL APPROACH MOVE ALARMS	ACTIVATE
SSCC ATCS ADDRESS	7ARRALL.GCG.07.01

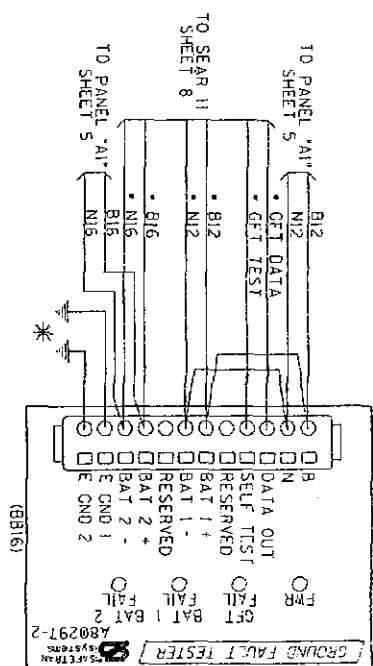

VERIFY THE BATTERY SUPPLY VOLTAGES	
B12 BATTERY VOLTAGE AT INPUT DC1	VOLT 1: .
B16 BATTERY VOLTAGE AT INPUT DC2	VOLT 2: .

NOTES:

ALL WIRING TO BE *ISAWG
UNLESS NOTED OTHERWISE

* = CABLE PROVIDED WITH SEAR II

** = OPTIONS: IF BELL SENSOR = 0,
THEN BELL FIELDS ARE NOT USED.


*** = IF SITE TYPE = NO COMMUNICATION,
THEN THESE OPTIONS ARE NOT
DISPLAYED

**** = THESE SETTINGS SHOULD BE LEFT
AT THE DEFAULT SETTING.

* = CONNECT *E CND 1* AND *E CND 2*
TO INDEPENDENT GROUND POINTS
ON SIDE A AND SIDE B.

SEAR II SET UP CHART & GROUND FAULT TESTER


DESIGNED BY:	WJK 01-06-07	NOFOLK SOUTHERN
DRAWN BY:	OFFICE OF ASST. VICE PRESIDENT	COMM. & SIGNAL, ATLANTA, GA.
CHECKED BY:	SWS 01-06-07	FILE R-1
IN SERVICE:	SEK 01-23-07	SPRINGFIELD, OH
CARD OF	DAYTON DISTRICT	FILE R-1
DWG. NO.	8211850.09	SHEET 9 of 19

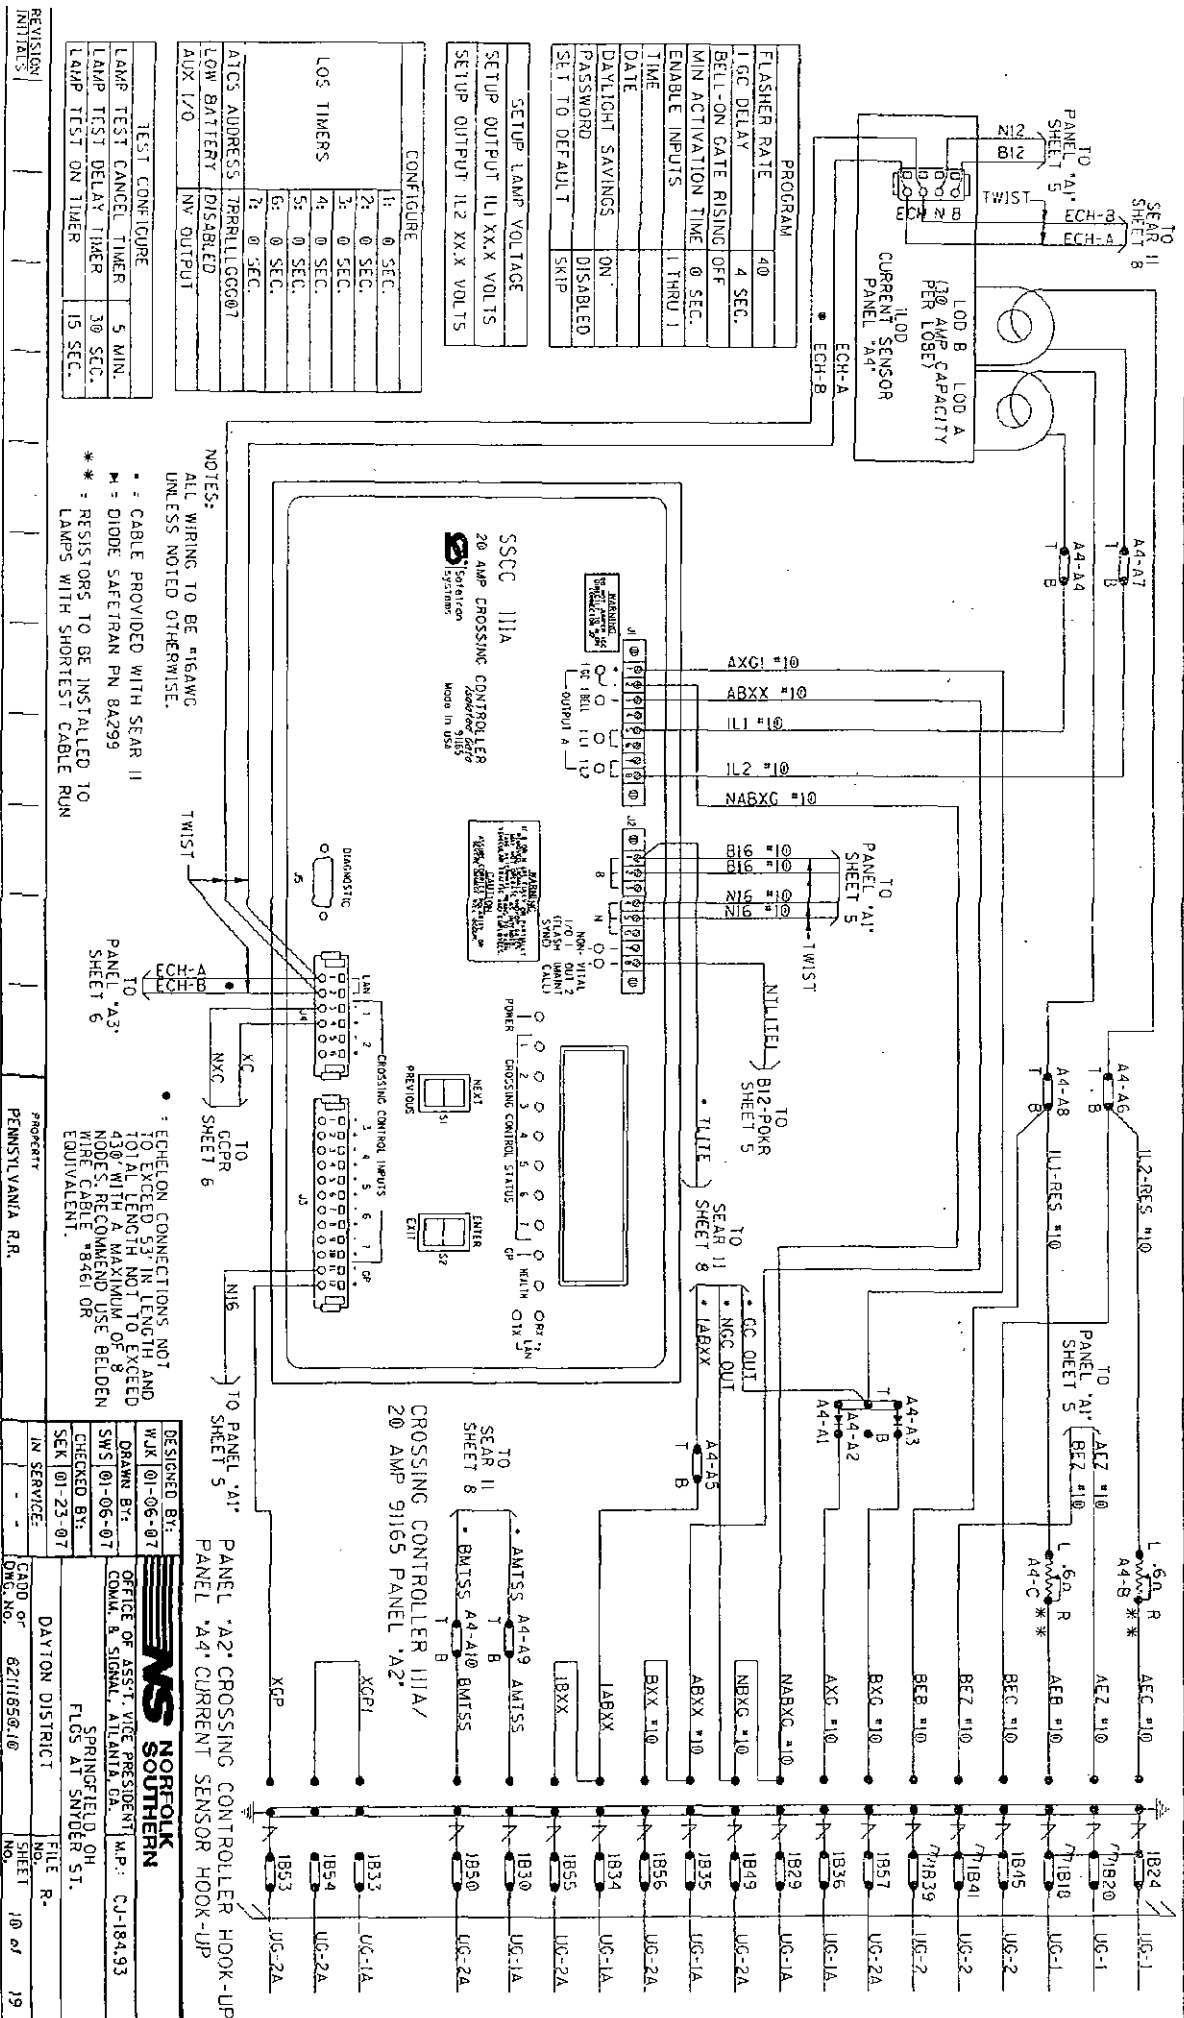

LEFT TWO ROWS TERMINAL BOARD 1

'1A'

'1B'

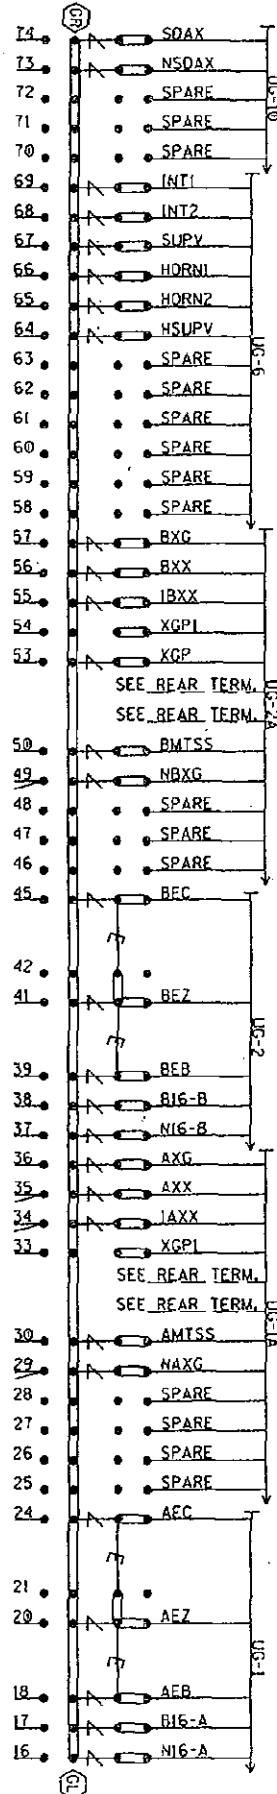

NOTE: INSTALL TEST LINKS ON ALL TRACK WIRES AND ON ALL LOW VOLTAGE UNDERGROUND CABLE TERMINATIONS.


SEE FARADAY SHIELD DETAILS - 1A & 1B FOR HOW THIS PORTION OF THE FARADAY SHIELD IS PREDRILLED. ONLY INSTALL AND USE THE TERMINALS NEEDED.

⚡ = Heavy Duty Squelizer (022100-1X)

⚡ = Lightning Arrester (022585-1X)

⚡ = LPC-10550-51

⚡ = TERMINALS GROUNDED TO SHIELD. 4 POST BLOCKS USE EITHER - CL - SERMI PART NO. 61278 CL - SERMI PART NO. 61278-1.



BACKBOARD DETAIL - 1A & 1B

REVISION 02-05-07

PROPERTY PENNSYLVANIA R.R.


DESIGNED BY:	WJK 01-06-07
DRAWN BY:	SWS 01-06-07
CHECKED BY:	SEK 01-23-07
IN SERVICE:	
CADD OF:	DAYTON DISTRICT
FILE NO.:	8211850.13
SHEET:	13 of 19

NORFOLK SOUTHERN
OFFICE OF ASSIST. VICE PRESIDENT
COMM. & SIGNAL, ATLANTA, GA.
SPRINGFIELD, OH
FLGS AT SNYDER ST.
M.P.: C-1184.93


"1B"

"1A"

(SEE PREVIOUS SHEET FOR OTHER WIRES IN CABLE)

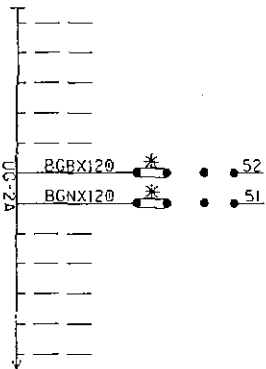

(SEE PREVIOUS SHEET FOR OTHER WIRES IN CABLE)

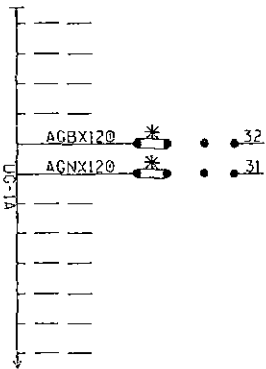

NOTE: ALL 120VAC AND ABOVE WILL BE WIRED TO THE REAR OF FARADAY BACKBOARD. INSULATED NUTS MUST BE USED ON ALL TERMINALS.

* = CLOSED DURING WINTER MONTHS

REAR OF FARADAY BACKBOARD
REAR BACKBOARD DETAIL - 1A & 1B

DESIGNED BY:	WJK 01-05-07	NS NORFOLK SOUTHERN
DRAWN BY:	OFFICE OF ASST. VICE PRESIDENT	
SWS 01-06-07	COMM. & SIGNAL, ATLANTA, GA.	
CHECKED BY:	FILE R -	
SEK 01-23-07	SPRINGFIELD, OH	
IN SERVICE:	DAYTON DISTRICT	
CADD OF	82111850.14	
DRG. NO.		
FILE R -		
SHEET	14 of	19

PROPERTY	PENNSYLVANIA R.R.
INITIALS	


TERMINAL BOARD I LEFT HALF

"1A"

"1B"

2" PANDUIT

2" PANDUIT

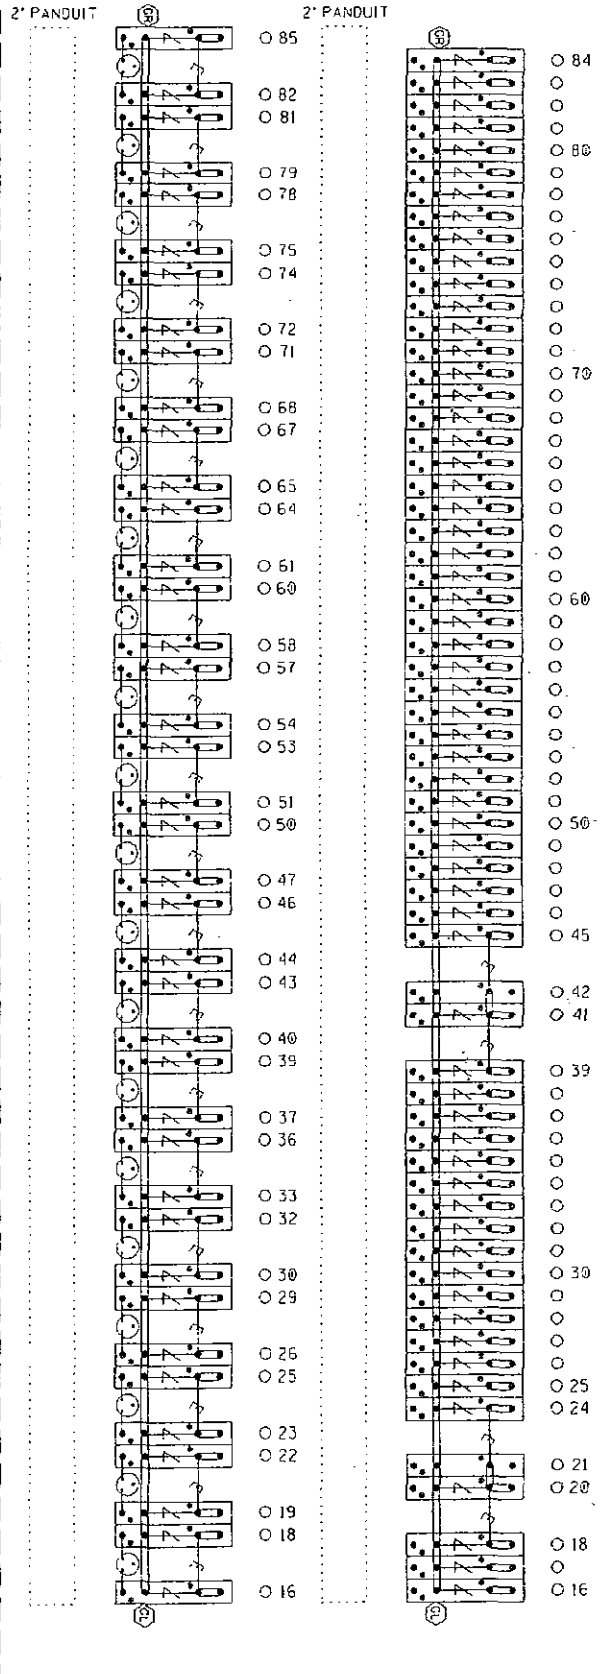

NOTE: IF THE FARADAY SHIELD WOULD EVER NEED TO BE DRILLED IN THE FIELD, PROPER PRECAUTIONS MUST BE TAKEN TO INSURE METAL SHAVINGS DO NOT GET INTO EXISTING TERMINALS/WIRES.

AREA BELOW IS SCALED WITH AS=75

INDICATES PLACEMENT OF PANDUIT

THIS SHEET IS FOR REFERENCE ONLY. TO REFLECT HOW THE FARADAY SHIELD IS PREDRILLED. ONLY INSTALL AND USE THE TERMINALS NEEDED.



TERMINALS GROUNDED TO SHIELD. 4 POST BLOCKS USE EITHER - GR - SERIAL PART NO. 61278 OR - SERIAL PART NO. 61278-1.



Clear view
= Lightning Arrester
(022585-1X)
LPC-10560-51



= Heavy Duty Equotizer
(022700-1X)

REVISION
INITIALS

PRIORITY
PENNSYLVANIA R.R.


DESIGNED BY:	WJK 01-06-07
DRAWN BY:	SWJ 01-06-07
CHECKED BY:	SEK 01-23-07
IN SERVICE:	
DATE OF	821185015
NO.	
SHEET	15 of 19
FILE NO.	
FILE R.	
FILE S.	
FILE T.	
FILE U.	
FILE V.	
FILE W.	
FILE X.	
FILE Y.	
FILE Z.	
FILE AA.	
FILE AB.	
FILE AC.	
FILE AD.	
FILE AE.	
FILE AF.	
FILE AG.	
FILE AH.	
FILE AI.	
FILE AJ.	
FILE AK.	
FILE AL.	
FILE AM.	
FILE AN.	
FILE AO.	
FILE AP.	
FILE AQ.	
FILE AR.	
FILE AS.	
FILE AT.	
FILE AU.	
FILE AV.	
FILE AW.	
FILE AX.	
FILE AY.	
FILE AZ.	
FILE BA.	
FILE BB.	
FILE BC.	
FILE BD.	
FILE BE.	
FILE BF.	
FILE BG.	
FILE BH.	
FILE BI.	
FILE BJ.	
FILE BK.	
FILE BL.	
FILE BM.	
FILE BN.	
FILE BO.	
FILE BP.	
FILE BQ.	
FILE BR.	
FILE BS.	
FILE BT.	
FILE BU.	
FILE BV.	
FILE BW.	
FILE BX.	
FILE BY.	
FILE BZ.	
FILE CA.	
FILE CB.	
FILE CC.	
FILE CD.	
FILE CE.	
FILE CF.	
FILE CG.	
FILE CH.	
FILE CI.	
FILE CJ.	
FILE CK.	
FILE CL.	
FILE CM.	
FILE CN.	
FILE CO.	
FILE CP.	
FILE CQ.	
FILE CR.	
FILE CS.	
FILE CT.	
FILE CU.	
FILE CV.	
FILE CW.	
FILE CX.	
FILE CY.	
FILE CZ.	
FILE DA.	
FILE DB.	
FILE DC.	
FILE DD.	
FILE DE.	
FILE DF.	
FILE DG.	
FILE DH.	
FILE DI.	
FILE DJ.	
FILE DK.	
FILE DL.	
FILE DM.	
FILE DN.	
FILE DO.	
FILE DP.	
FILE DQ.	
FILE DR.	
FILE DS.	
FILE DT.	
FILE DU.	
FILE DV.	
FILE DW.	
FILE DX.	
FILE DY.	
FILE DZ.	
FILE EA.	
FILE EB.	
FILE EC.	
FILE ED.	
FILE EE.	
FILE EF.	
FILE EG.	
FILE EH.	
FILE EI.	
FILE EJ.	
FILE EK.	
FILE EL.	
FILE EM.	
FILE EN.	
FILE EO.	
FILE EP.	
FILE EQ.	
FILE ER.	
FILE ES.	
FILE ET.	
FILE EU.	
FILE EV.	
FILE EW.	
FILE EX.	
FILE EY.	
FILE EZ.	
FILE FA.	
FILE FB.	
FILE FC.	
FILE FD.	
FILE FE.	
FILE FF.	
FILE FG.	
FILE FH.	
FILE FI.	
FILE FJ.	
FILE FK.	
FILE FL.	
FILE FM.	
FILE FN.	
FILE FO.	
FILE FP.	
FILE FQ.	
FILE FR.	
FILE FS.	
FILE FT.	
FILE FU.	
FILE FV.	
FILE FW.	
FILE FX.	
FILE FY.	
FILE FZ.	
FILE GA.	
FILE GB.	
FILE GC.	
FILE GD.	
FILE GE.	
FILE GF.	
FILE GG.	
FILE GH.	
FILE GI.	
FILE GJ.	
FILE GK.	
FILE GL.	
FILE GM.	
FILE GN.	
FILE GO.	
FILE GP.	
FILE GQ.	
FILE GR.	
FILE GS.	
FILE GT.	
FILE GU.	
FILE GV.	
FILE GW.	
FILE GX.	
FILE GY.	
FILE GZ.	
FILE HA.	
FILE HB.	
FILE HC.	
FILE HD.	
FILE HE.	
FILE HF.	
FILE HG.	
FILE HH.	
FILE HI.	
FILE HJ.	
FILE HK.	
FILE HL.	
FILE HM.	
FILE HN.	
FILE HO.	
FILE HP.	
FILE HQ.	
FILE HR.	
FILE HS.	
FILE HT.	
FILE HU.	
FILE HV.	
FILE HW.	
FILE HX.	
FILE HY.	
FILE HZ.	
FILE IA.	
FILE IB.	
FILE IC.	
FILE ID.	
FILE IE.	
FILE IF.	
FILE IG.	
FILE IH.	
FILE II.	
FILE IJ.	
FILE IK.	
FILE IL.	
FILE IM.	
FILE IN.	
FILE IO.	
FILE IP.	
FILE IQ.	
FILE IR.	
FILE IS.	
FILE IT.	
FILE IU.	
FILE IV.	
FILE IW.	
FILE IX.	
FILE IY.	
FILE IZ.	
FILE JA.	
FILE JB.	
FILE JC.	
FILE JD.	
FILE JE.	
FILE JF.	
FILE JG.	
FILE JH.	
FILE JI.	
FILE JJ.	
FILE JK.	
FILE JL.	
FILE JM.	
FILE JN.	
FILE JO.	
FILE JP.	
FILE JQ.	
FILE JR.	
FILE JS.	
FILE JT.	
FILE JU.	
FILE JV.	
FILE JW.	
FILE JX.	
FILE JY.	
FILE JZ.	
FILE KA.	
FILE KB.	
FILE KC.	
FILE KD.	
FILE KE.	
FILE KF.	
FILE KG.	
FILE KH.	
FILE KI.	
FILE KJ.	
FILE KK.	
FILE KL.	
FILE KM.	
FILE KN.	
FILE KO.	
FILE KP.	
FILE KQ.	
FILE KR.	
FILE KS.	
FILE KT.	
FILE KU.	
FILE KV.	
FILE KW.	
FILE KX.	
FILE KY.	
FILE KZ.	
FILE LA.	
FILE LB.	
FILE LC.	
FILE LD.	
FILE LE.	
FILE LF.	
FILE LG.	
FILE LH.	
FILE LI.	
FILE LJ.	
FILE LK.	
FILE LL.	
FILE LM.	
FILE LN.	
FILE LO.	
FILE LP.	
FILE LQ.	
FILE LR.	
FILE LS.	
FILE LT.	
FILE LU.	
FILE LV.	
FILE LW.	
FILE LX.	
FILE LY.	
FILE LZ.	
FILE MA.	
FILE MB.	
FILE MC.	
FILE MD.	
FILE ME.	
FILE MF.	
FILE MG.	
FILE MH.	
FILE MI.	
FILE MJ.	
FILE MK.	
FILE ML.	
FILE MM.	
FILE MN.	
FILE MO.	
FILE MP.	
FILE MQ.	
FILE MR.	
FILE MS.	
FILE MT.	
FILE MU.	
FILE MV.	
FILE MW.	
FILE MX.	
FILE MY.	
FILE MZ.	
FILE NA.	
FILE NB.	
FILE NC.	
FILE ND.	
FILE NE.	
FILE NF.	
FILE NG.	
FILE NH.	
FILE NI.	
FILE NJ.	
FILE NK.	
FILE NL.	
FILE NM.	
FILE NN.	
FILE NO.	
FILE NP.	
FILE NQ.	
FILE NR.	
FILE NS.	
FILE NT.	
FILE NU.	
FILE NV.	
FILE NW.	
FILE NX.	
FILE NY.	
FILE NZ.	
FILE OA.	
FILE OB.	
FILE OC.	
FILE OD.	
FILE OE.	
FILE OF.	
FILE OG.	
FILE OH.	
FILE OI.	
FILE OJ.	
FILE OK.	
FILE OL.	
FILE OM.	
FILE ON.	
FILE OO.	
FILE OP.	
FILE OQ.	
FILE OR.	
FILE OS.	
FILE OT.	
FILE OU.	
FILE OV.	
FILE OW.	
FILE OX.	
FILE OY.	
FILE OZ.	
FILE PA.	
FILE PB.	
FILE PC.	
FILE PD.	
FILE PE.	
FILE PF.	
FILE PG.	
FILE PH.	
FILE PI.	
FILE PJ.	
FILE PK.	
FILE PL.	
FILE PM.	
FILE PN.	
FILE PO.	
FILE PP.	
FILE PQ.	
FILE PR.	
FILE PS.	
FILE PT.	
FILE PU.	
FILE PV.	
FILE PW.	
FILE PX.	
FILE PY.	
FILE PZ.	
FILE QA.	
FILE QB.	
FILE QC.	
FILE QD.	
FILE QE.	
FILE QF.	
FILE QG.	
FILE QH.	
FILE QI.	
FILE QJ.	
FILE QK.	
FILE QL.	
FILE QM.	
FILE QN.	
FILE QO.	
FILE QP.	
FILE QQ.	
FILE QR.	
FILE QS.	
FILE QT.	
FILE QU.	
FILE QV.	
FILE QW.	
FILE QX.	
FILE QY.	
FILE QZ.	
FILE RA.	
FILE RB.	
FILE RC.	
FILE RD.	
FILE RE.	
FILE RF.	
FILE RG.	
FILE RH.	
FILE RI.	
FILE RJ.	
FILE RK.	
FILE RL.	
FILE RM.	
FILE RN.	
FILE RO.	
FILE RP.	
FILE RQ.	
FILE RR.	
FILE RS.	
FILE RT.	
FILE RU.	
FILE RV.	
FILE RW.	
FILE RX.	
FILE RY.	
FILE RZ.	
FILE SA.	
FILE SB.	
FILE SC.	
FILE SD.	
FILE SE.	
FILE SF.	
FILE SG.	
FILE SH.	
FILE SI.	
FILE SJ.	
FILE SK.	
FILE SL.	
FILE SM.	
FILE SN.	
FILE SO.	
FILE SP.	
FILE SQ.	
FILE SR.	
FILE SS.	
FILE ST.	
FILE SU.	
FILE SV.	
FILE SW.	
FILE SX.	
FILE SY.	
FILE SZ.	
FILE TA.	
FILE TB.	
FILE TC.	
FILE TD.	
FILE TE.	
FILE TF.	
FILE TG.	
FILE TH.	
FILE TI.	
FILE TJ.	
FILE TK.	
FILE TL.	
FILE TM.	
FILE TN.	
FILE TO.	
FILE TP.	
FILE TQ.	
FILE TR.	
FILE TS.	
FILE TT.	
FILE TU.	
FILE TV.	
FILE TW.	
FILE TX.	
FILE TY.	
FILE TZ.	
FILE UA.	
FILE UB.	
FILE UC.	
FILE UD.	
FILE UE.	
FILE UF.	
FILE UG.	
FILE UH.	
FILE UI.	
FILE UJ.	
FILE UK.	
FILE UL.	
FILE UM.	
FILE UN.	
FILE UO.	
FILE UP.	
FILE UQ.	
FILE UR.	
FILE US.	
FILE UT.	
FILE UY.	
FILE UZ.	
FILE VA.	
FILE VB.	
FILE VC.	
FILE VD.	
FILE VE.	
FILE VF.	
FILE VG.	
FILE VH.	
FILE VI.	
FILE VJ.	
FILE VK.	
FILE VL.	
FILE VM.	
FILE VN.	
FILE VO.	
FILE VP.	
FILE VQ.	
FILE VR.	
FILE VS.	
FILE VT.	
FILE VY.	
FILE VZ.	
FILE WA.	
FILE WB.	
FILE WC.	
FILE WD.	
FILE WE.	
FILE WF.	
FILE WG.	
FILE WH.	
FILE WI.	
FILE WJ.	
FILE WK.	
FILE WL.	
FILE WM.	
FILE WN.	
FILE WO.	
FILE WP.	
FILE WQ.	
FILE WR.	
FILE WS.	
FILE WT.	
FILE WY.	
FILE WZ.	
FILE XA.	
FILE XB.	
FILE XC.	
FILE XD.	
FILE XE.	
FILE XF.	
FILE XG.	
FILE XH.	
FILE XI.	
FILE XJ.	
FILE XK.	
FILE XL.	
FILE XM.	
FILE XN.	
FILE XO.	
FILE XP.	
FILE XQ.	
FILE XR.	
FILE XS.	
FILE XT.	
FILE XZ.	
FILE YA.	
FILE YB.	
FILE YC.	
FILE YD.	
FILE YE.	
FILE YF.	
FILE YG.	
FILE YH.	
FILE YI.	
FILE YJ.	
FILE YK.	
FILE YL.	
FILE YM.	
FILE YN.	
FILE YO.	
FILE YP.	
FILE YQ.	
FILE YR.	
FILE YS.	
FILE YT.	
FILE YZ.	
FILE ZA.	
FILE ZB.	
FILE ZC.	
FILE ZD.	
FILE ZE.	
FILE ZF.	
FILE ZG.	

TERMINAL BOARD 1 RIGHT HALF

"1C"

NOTE: IF THE FARADAY SHIELD WOULD EVER NEED TO BE DRILLED IN THE FIELD, PROPER PRECAUTIONS MUST BE TAKEN TO INSURE METAL SHAVINGS DO NOT GET INTO EXISTING TERMINALS/WIRES.

AREA BELOW IS SCALED WITH A=75

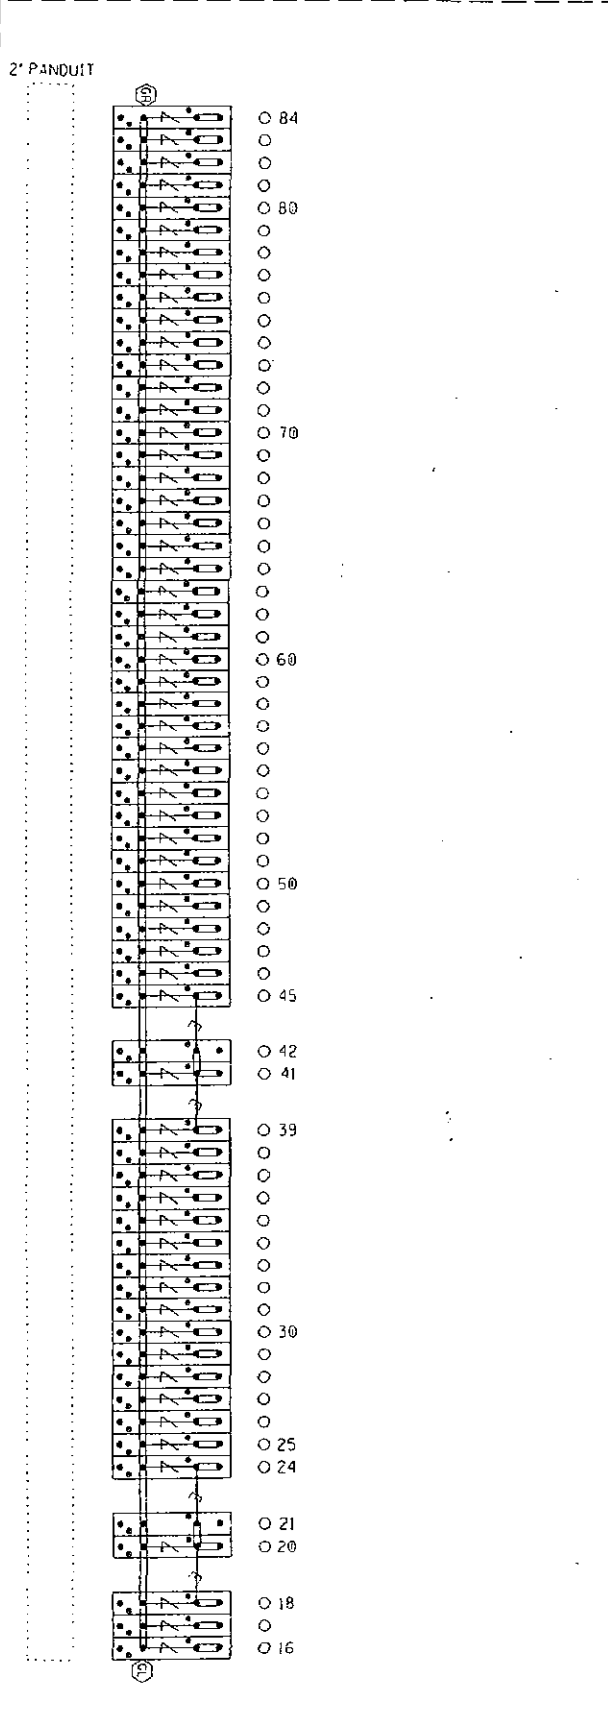

⌋ = Heavy Duty Equalizer
(022700-1X)

⌋ = Clearview
Lighting Arrestor
(022585-1X)

⌋ = LPC-10560-51

⌋ = TERMINALS GROUNDED TO SHIELD.
4 POST BLOCKS USE EITHER -
GR - SERMAN PART NO. 61278
GL - SERMAN PART NO. 61278-1.

INDICATES PLACEMENT
OF PANDUIT

THIS SHEET IS FOR REFERENCE ONLY.
TO REFLECT HOW THE FARADAY SHIELD
IS PREDRILLED, ONLY INSTALL AND USE
THE TERMINALS NEEDED.

REVISION INITIALS	PROPERTY	DESIGNED BY:	DATE	CADW OF	FILE NO.	SHEET	15 of	19
	PENNSYLVANIA R.R.	WJK 01-06-07		DAYTON DISTRICT	821185016			
		DRAWN BY:						
		SWS 01-06-07						
		CHECKED BY:						
		SEK 01-23-07						
		IN SERVICE:						

TERMINAL BOARD 1
RIGHT ROW
FARADAY SHIELD DETAIL - 1C


NORFOLK SOUTHERN

OFFICE OF ASST. VICE PRESIDENT
COMM. & SIGNAL, ATLANTA, GA.

SPRINGFIELD, OH
FLGS AT SNYDER ST.

DATE: 01-18-93

FILE NO. R-
SHEET 15 of 19

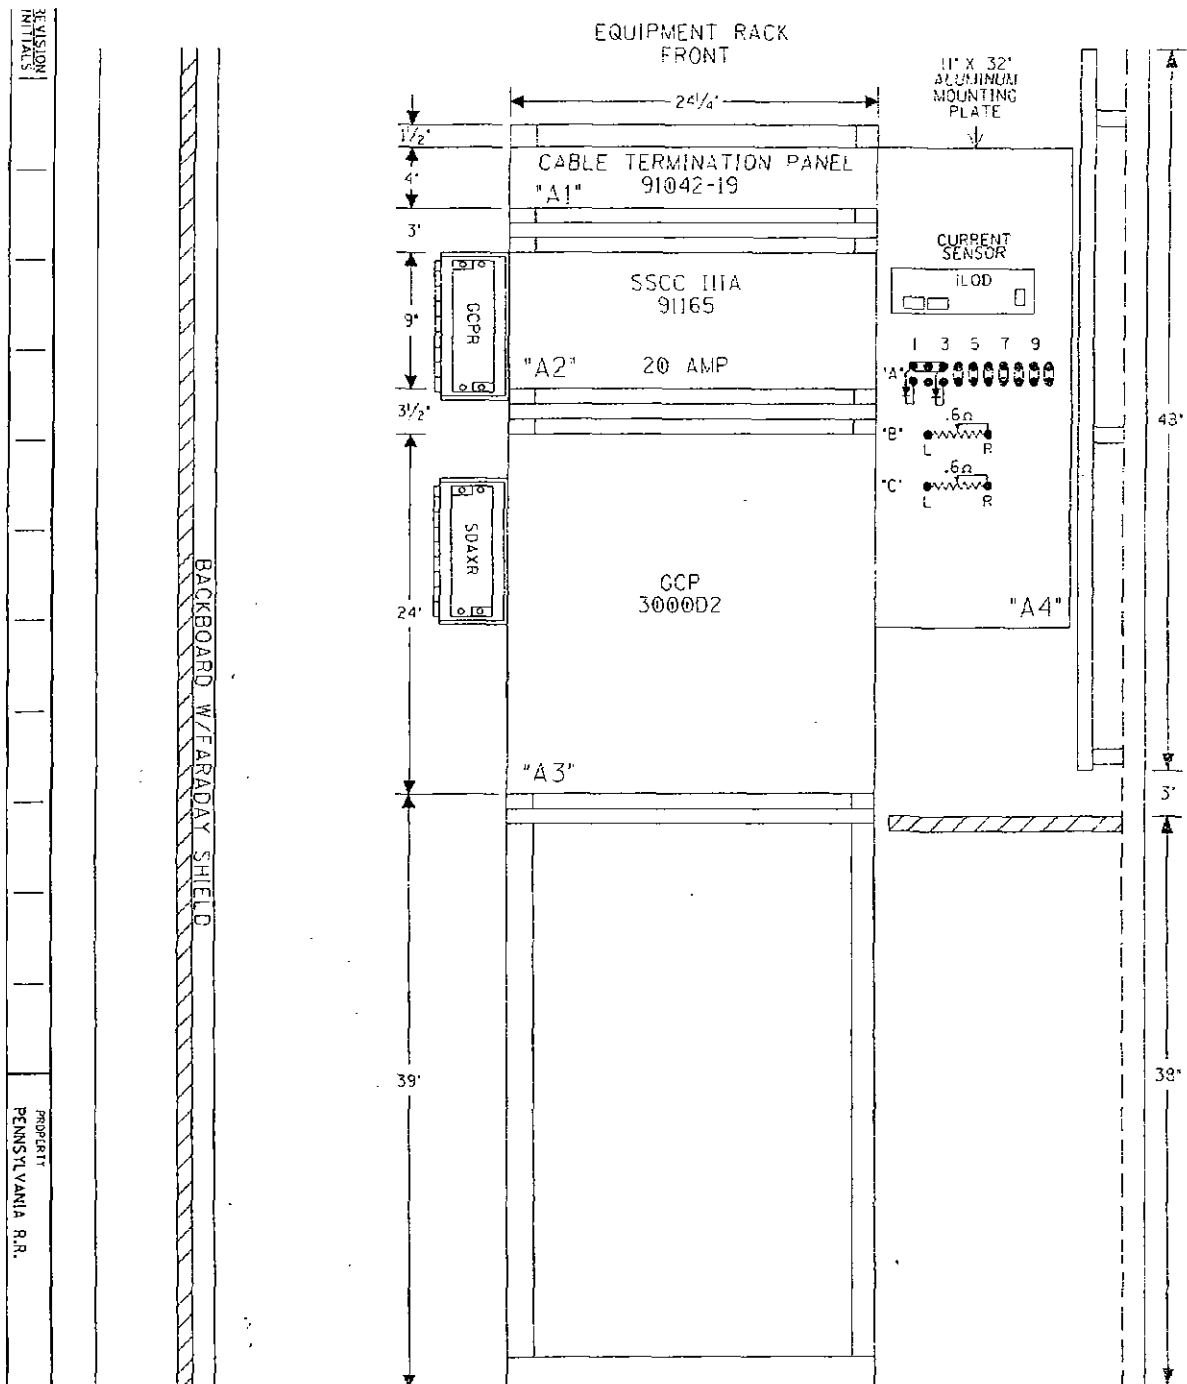

DESIGNED BY: WJK 01-06-07

DRAWN BY: SWS 01-06-07

CHECKED BY: SEK 01-23-07

IN SERVICE:

DAYTON DISTRICT

FILE R-17 of 19

PROPERTY

PENNSYLVANIA R.R.

BACKBOARD W/FARADAY SHIELD

SAFETRAN ALSTOM(GRS) RELAY CROSS REFERENCE LIST

SAFETRAN ALSTOM(GRS)

400003 - A62-308

RACK PLACEMENT

6' X 6' HOUSE - SIDE "C"

0 3 6 9

1 FT 2 FT 3 FT

DESIGNED BY: WJK 01-06-07

DRAWN BY: SWS 01-06-07

CHECKED BY: SEK 01-23-07

IN SERVICE:

DAYTON DISTRICT

FILE R-17 of 19

OFFICE OF ASS'T. VICE PRESIDENT/ M.P.: CJ-184.93

COMM. & SIGNAL, ATLANTA, GA.

SPRINGFIELD, OH.


FLGS AT SNYDER ST.

CCPR

SDAXR


400003

400003

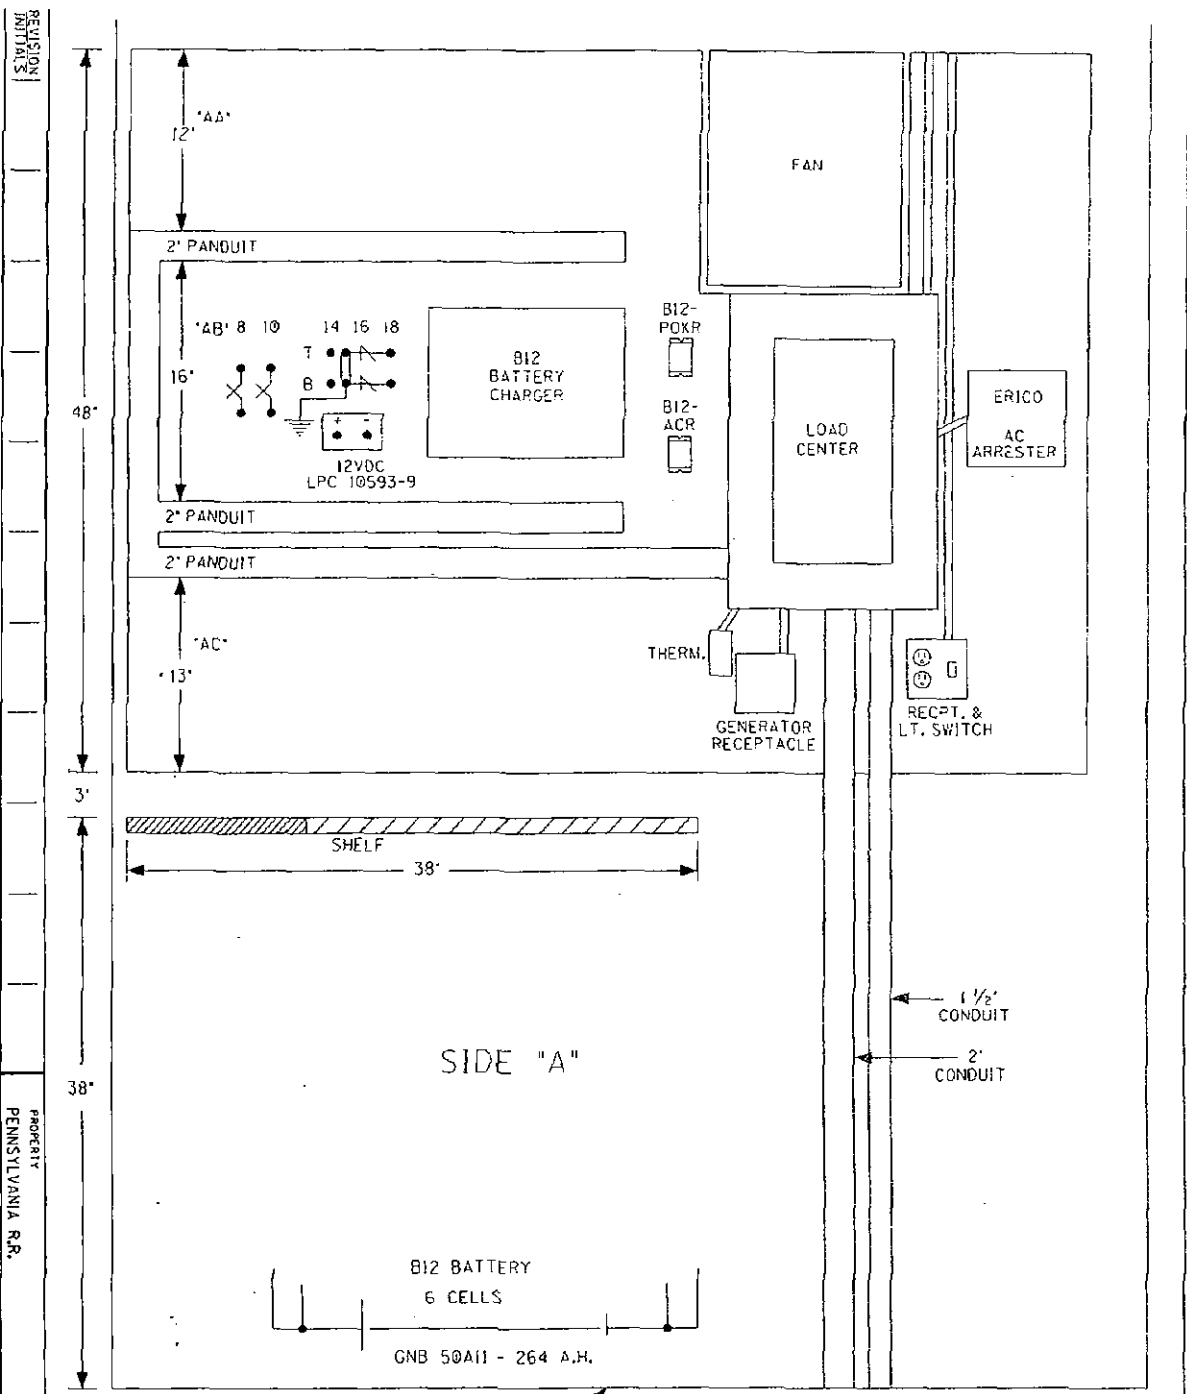

DESIGNED BY:	WJK 01-06-07	OFFICE OF ASST. VICE PRESIDENT	W.P.: CU-184.93
DRAWN BY:	SWS 01-06-07	COMM. & SIGNAL, ATLANTA, GA.	
CHECKED BY:	SEK 01-23-07	SPRINGFIELD, OH.	
IN SERVICE:		FLGS AT SNYDER ST.	
CADD OF:	DAYTON DISTRICT	FILE R-	
DWG. NO.:	8211850.18	SHEET	18 of 19

6' X 6' HOUSE - SIDE "A"



REVISION
INITIALS

PROPERTY
PENNSYLVANIA R.R.

