97-392-GA-BNR

Form 217
OHIO POWER SITING BOARD

0001

Operator EAST OHIO GAS

One Time Notification

Date of Report April 3, 1997 Job No. CJO #21531

Construction Location Pine Lake Road (Street) Springfield (City, Village or Township) Mahoning (County)

Proposed Dates: Starting May 1, 1997 Completion August 31, 1997

Actual Dates: Starting Completion

Class Location 1 Replacement Yes New Construction

MAOP 595 psig Design Pressure of Weakest Element 720 psig Normal Operating Pressure 400 psig

	Size	Length	Wall Thickness	Grade	Anode	Rectifier
Steel	26"	100'	.375	X-42	No	Yes

			SRD	Density (M.D., H.D.)		
Plastic						

Note: Please attach sheet if more space is needed.

Description of Project Install four 45 degree ells to lower pipe in creek

Estimated Cost $24,500 See Attached Prints X Cover Letter

Return to:

Ohio Power Siting Board
The Public Utilities Commission of Ohio
The Borden Building, 12th Floor
180 East Broad Street
Columbus, Ohio 43215-3793

Attn: Ron Yerian

Company Contact for More Information Maureen C. Critchfield

Title Engineering & Construction Supervisor

Street Address 7015 Freedom Avenue NW

City, State, Zip Code North Canton, Ohio 44720

Telephone (330) 497-5131

Signature Maureen C. Critchfield

File: OPSB 7

This is to certify that the images appearing are an accurate and complete reproduction of a case file document delivered in the regular course of business.
Technician [illegible] Date Processed April 9, 1997

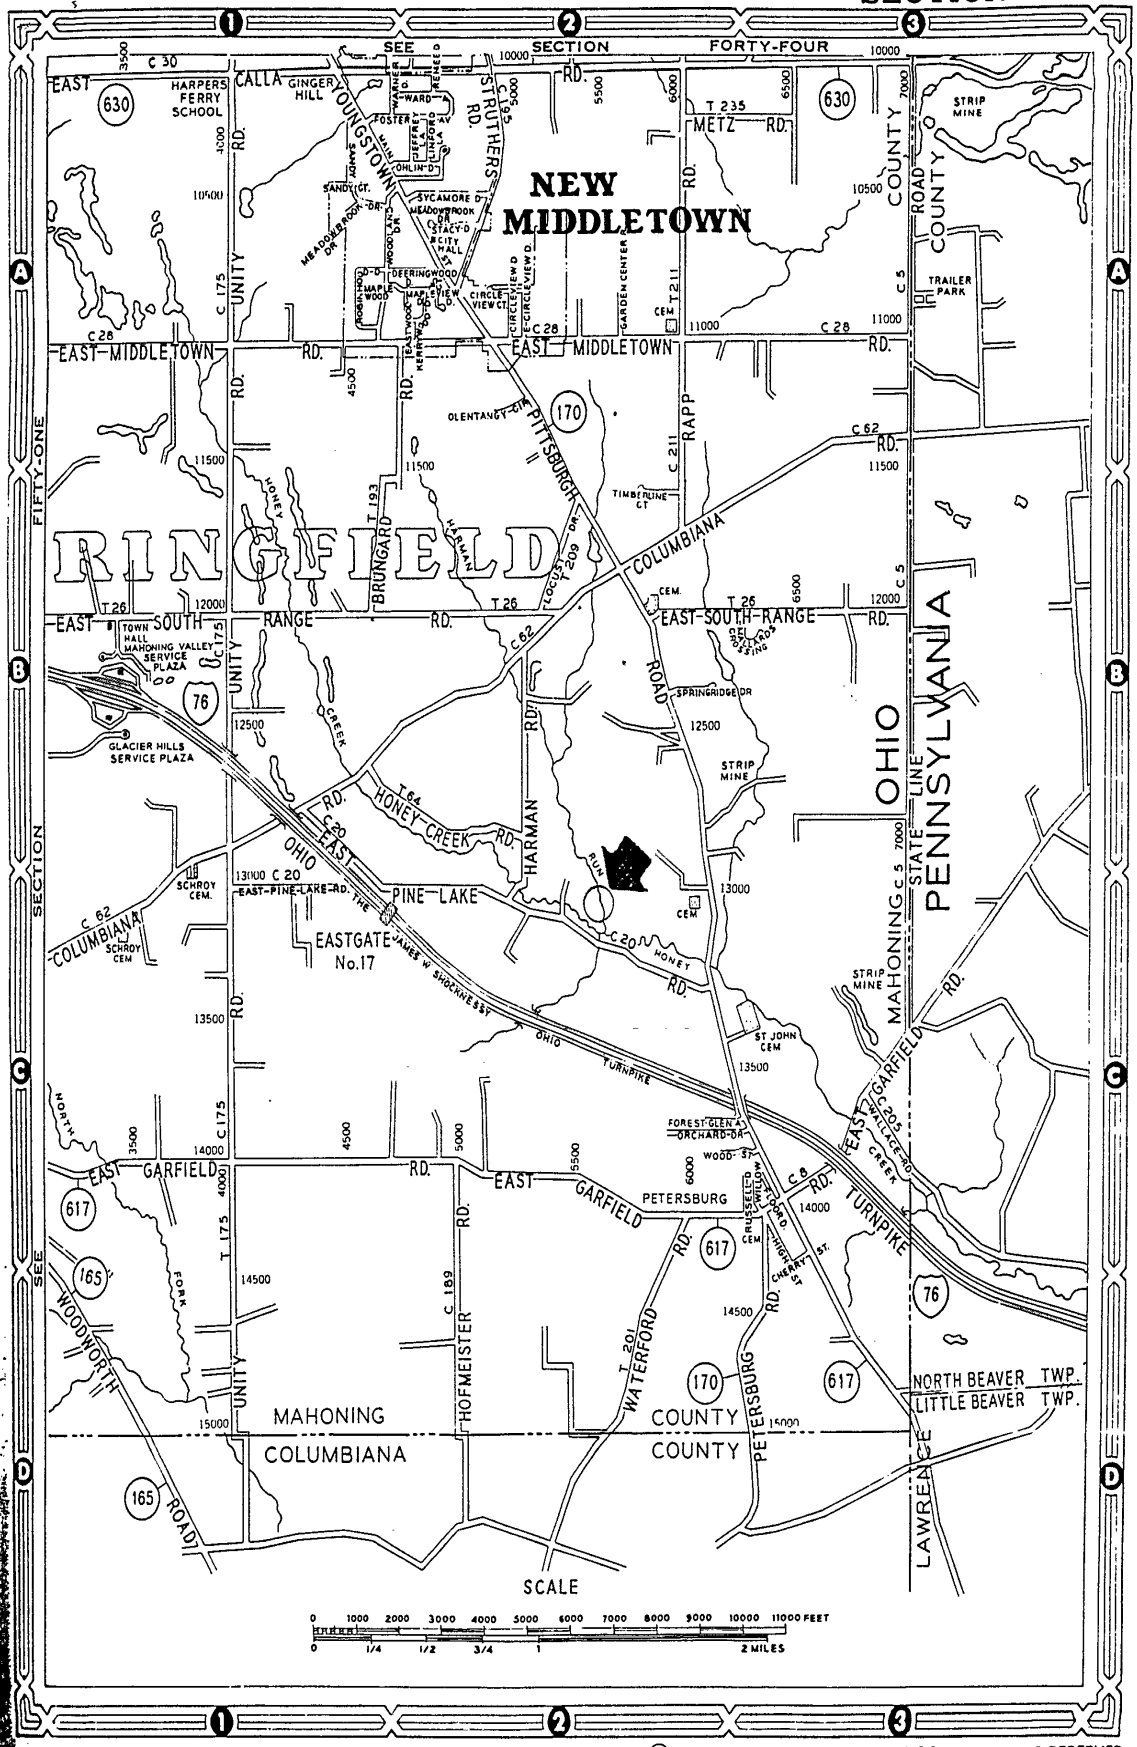

COPYRIGHTED © BY COMMERCIAL SURVEY CO. ALL RIGHTS RESERVED
